

ANNUAL REPORT OF CONSTRUCTION AND REPAIR

Fiscal year ending June 30, 1940

[illegible]

First----- (C. A.) (Dept.) Station Fort-~~Revere~~, Mass.

ANNUAL REPORT OF CONSTRUCTION AND REPAIR

Fiscal year ending June 30, 19 39

(1) BUILD- ING NO.	(2) DESIGNATION OF BUILDINGS OR SYSTEMS	(3) BRIEF DESCRIPTION OF IMPORTANT REPAIR WORK ACCOMPLISHED DURING THE FISCAL YEAR, COSTING \$100 OR MORE	(4) REPAIR EXPENDITURES FOR THE PRESENT FISCAL YEAR	(5) TOTAL REPAIR EXPENDITURES FROM THE DATE THE BUILD- ING OR SYSTEM WAS CONSTRUCTED TO JUNE 30, PRESENT FISCAL YEAR	(6) TOTAL ORIGINAL COST, NOT INCLUDING REPAIRS, TO JUNE 30, PRESENT FISCAL YEAR	(7) COST OF NEW CON- STRUCTION (INCLUDING ALTERATIONS AND ADDITIONS BUT NOT REPAIRS) DURING THE PRESENT FISCAL YEAR	(8) REPLACEMENT VALUE JUNE 30, 19 39 PRESENT FISCAL YEAR
	Perm. Buildings		\$	\$	\$	\$	\$
	Officers Quarters						
✓ 2&2A	" "	Renovation of Electric Wiring \$116.49					
		Replacement of Electric Light Entrance					
		Service \$155.74 Interior Painting \$423.71	1,022 41	11,849 50	11,492 00		12,827 00
	Sub Total		1,022 41	11,849 50	11,492 00		12,827 00
	N.C.O. Quarters						
✓ 15&15A	" "			1,837 19	5,664 00		8,000 00
✓ 16&16A	" "	Repairs to Porch Roof \$217.39					
		Replacement of Electric Light Entrance					
		Service \$164.18	555 00	6,330 46	5,664 00		8,000 00
	Sub Total		555 00	8,167 65	11,328 00		16,000 00
	Storehouses						
✓ 10	✓ Ordnance			1,482 05	2,800 00		3,200 00
✓ 19	✓ Quartermaster		175 91	3,892 89	14,352 76		16,413 50
✓ 43	✓ Artillery Eng.		49 60	189 34	5,153 09		6,400 00
	Sub Total		225 51	5,564 28	22,305 85		26,013 50
	Misc. Buildings						
✓ 11	✓ Bakery			384 46	2,530 00		2,400 00
✓ 13	✓ Guard House			781 52	2,950 00		3,200 00
✓ 7A	✓ Q.M. Sealer				Unknown		480 00
✓ 44	✓ Reservation Fence	Replacement of Fence \$9,992.15	62 95	62 95	10,055 10	9,992 15	6,000 00
✓ 22	✓ Searchlight Shed			91 88	761 00		800 00
✓ 18	✓ Water Tower	Repairs to Roof \$150.74	299 20	1,178 15	12,012 00		16,000 00
	Sub Total		362 15	2,498 96	28,308 10	9,992 15	28,880 00
	Misc. Utilities						
	Fire Equipment		91	13 97	538 00		480 00
	Grounds	Regrading \$139.35					
		Care & Improvement \$154.22	308 27	1,658 17	256,399 35		132,000 00
	Heavy Furniture			50 86	156 50		150 00
	Ranges, Coal		29 81	76 86	247 48		248 00
	Roads			211 40	Unknown		2,670 00
	Sewer Mains		92 36	114 51	"		7,580 77
	Stoves, Heating				44 90		40 00
	Refrigerators		22 79	2279	333 75		365 00
	Street Lights			286 57	Unknown		1,091 25
	Walks			539 02	"		850 00
	Water Mains	Replacement of Hydrant \$138.69	148 92	650 02	"		1,349 02
	Sub Total		603 06	3,624 17	257,719 98		146,824 04
	Grand Total		2,768 13	31,706 56	331,153 93		230,544 54

TOTAL

ANNUAL REPORT OF CONSTRUCTION AND REPAIR

Fiscal year ending June 30, 19 41

(1) BUILD- ING NO.	(2) DESIGNATION OF BUILDINGS OR SYSTEMS	(3) BRIEF DESCRIPTION OF IMPORTANT REPAIR WORK ACCOMPLISHED DURING THE FISCAL YEAR, COSTING \$100 OR MORE	(4) REPAIR EXPENDITURES FOR THE PRESENT FISCAL YEAR		(5) TOTAL REPAIR EXPENDITURES FROM THE DATE THE BUILD- ING OR SYSTEM WAS CONSTRUCTED TO JUNE 30, PRESENT FISCAL YEAR		(6) TOTAL ORIGINAL COST, NOT INCLUDING REPAIRS, TO JUNE 30, PRESENT FISCAL YEAR		(7) COST OF NEW CON- STRUCTION (INCLUDING ALTERATIONS AND ADDITIONS BUT NOT REPAIRS) DURING THE PRESENT FISCAL YEAR		(8) REPLACEMENT VALUE JUNE 30, 19..... PRESENT FISCAL YEAR	
	Perm. Bldgs.		\$		\$		\$		\$		\$	
2,2A	Officers Qtrs.		64	89	12986	01	11492	00			12827	00
	Sub-Total		64	89	12986	01	11492	00			12827	00
	Emer. Bldgs.											
T-2	Officers Qtrs.		36	44	36	44	15565	00	15565	00	15565	00
	Sub-Total		36	44	36	44	15565	00	15565	00	15565	00
	Perm. Bldgs.											
15,15A	NCO Qtrs.				1837	19	5664	00			8000	00
16,16A	" "				6591	91	5664	00			8000	00
	Sub-Total				8429	10	11328	00			16000	00
	Emer. Bldgs.											
T-9	Barracks		8	94	8	94	9117	00	9117	00	9117	00
T-10	"		7	77	7	77	9117	00	9117	00	9117	00
T-14	"		11	10	11	10	9117	00	9117	00	9117	00
T-15	"		7	76	7	76	9117	00	9117	00	9117	00
T-17	"		28	07	28	07	9117	00	9117	00	9117	00
T-18	"		28	07	28	07	9117	00	9117	00	9117	00
T-19	"		10	39	10	39	9117	00	9117	00	9117	00
T-20	"		6	59	6	59	9117	00	9117	00	9117	00
T-24	"		18	69	18	69	9117	00	9117	00	9117	00
T-25	"		10	22	10	22	9117	00	9117	00	9117	00
	Sub-Total		137	60	137	60	91170	00	91170	00	91170	00
	Perm. Bldgs.											
10	Ord. Storehouse				1482	05	2800	00			3200	00
19	QM " Replacing Heater \$396.33		599	78	4983	17	14352	76			16413	50
	Sub-Total		599	78	6465	22	17152	76			19613	50
	Emer. Bldgs.											
T-6	Storehouse						4635	00	4635	00	4635	00
T-7	"						2371	00	2371	00	2371	00
	Sub-Total						7006	00	7006	00	7006	00
	Perm. Misc. Bldgs.											
11	Bakery				384	46	2530	00			2400	00
13	Guardhouse				799	58	2950	00			3200	00
7A	QM Scales						Unknown				480	00
44	Reservation Fence				62	95	9992	15			6000	00
22	Searchlight Shed				91	88	761	00			800	00
18	Water Tower				1521	92	12012	00			16000	00
	Sub-Total				2860	79	28245	15			28880	00
	Emer. Misc. Bldgs.											
T-1	Theatre		77	05	77	05	12193	00	12193	00	12193	00
T-3	Day Room (Adm.)						5074	00	5074	00	5074	00
T-4	Infirmary		8	54	8	54	7280	00	7280	00	7280	00
T-5	Day Room						3795	00	3795	00	3795	00
T-8	Co. Adm. Bldg. (2)		7	44	7	44	5854	00	5854	00	5854	00
T-11	Fire House						1411	00	1411	00	1411	00
T-12	Post Exchange						9470	00	9470	00	9470	00
T-13	Mess Hall		64	56	64	56	6189	00	6189	00	6189	00
TOTAL												

[illegible]

Date June 30, 1940

RECORD OF EQUIPMENT AND CONDITION OF BUILDINGS

Date June 30, 1940

Reservation—Area 75.065 acres.

Name Fort Revere, Mass. Location Hull, Mass. Established 1900 Government-owned 75.065 acres. Leased 0 acres.

Character of post Coast Artillery Telegraph station Hingham, Mass. Freight station Nantasket, Mass.

Capacity: Officers 2; N. C. O. 4; Enl. men 0; Animals 0; Motor veh. 0; Hosp. beds 0

[illegible]

RECORD OF EQUIPMENT AND CONDITION OF BUILDINGS

Date June 30, 1939. Reservation—Area 75.065 acres.
Name Fort Revere, Mass. Location Hull, Mass. Established 1900 Government-owned 75.065 acres. Leased 0 acres.
Character of post Coast Artillery Telegraph station Hingham, Mass. Freight station Nantasket, Mass.
Capacity: Off. 2; W. off. and ft. cls. 0; N. C. O. 4; Enl. men 0; Animals 0; Motor veh. 0; Hosp. beds 0

POST BLDG. No.	DESIGNATION OF BUILDING	Laundry Stoves	HOT-WATER HEATERS					Range Boilers	RANGES OR COOKERS					METERS					Toilets	Urinals	Kitchen Sinks	Washbasins	Laundry Tubs	Shower Baths	Bathtubs	Fire Extinguishers	Fire Buckets	Storm Windows	Screens	Present Capacity CAPACITY Present Occupancy*	REMARKS ON CONDITION OF BUILDINGS	
			Coal	Oil	Gas	Steam	Electric		Coal	Oil	Gas	Steam	Electric	Water	Gas	Oil	Steam	Electric														
	Perm. Buildings																															
✓ 2&2A	Officers Quarters							2	2									2	3		4	2	4		2	2		46	46	2-Family*	Good M-1	
✓ 15&15A	N.C.O. Quarters							1	1									2	2		2	2	4		2			22	8	2-Family	Fair O-1	
✓ 10	Ordnance Storehouse																	1										8		2252 sq ft	Fair O-1	
✓ 16&16A	N.C.O. Quarters							2	2									2	2		2	2	4		2	2		24	24	2-Family*	Good M-1	
✓ 19	Q.M. Storehouse																	1	1			1								6885 sq ft	Good M-1	
✓ 43	Arty Engr Storehouse																														707 sq ft	Good M-1
✓ 11	Bakery																	1										9		1-Oven	Fair O-2	
✓ 13	Guardhouse																	1	2	2		2						9		2-Prisoners	Fair O-1	
✓ 22	Searchlight Shed																														1-Truck	Fair O-2
✓ 18	Water Tower																														117504 gals.	Good M-1
✓ 7-A	Quartermaster Stores																														20000 lbs.	Poor O-2
44	Reservation Fence																														6785 lin. ft.	Good O-1
Note:																																
M-Authorized for maintenance																																
O-Not authorized for maintenance																																
1-Actually habitable and useable																																
2-Habitable and useable only after expenditure of considerable funds.																																

RECORD OF EQUIPMENT AND CONDITION OF UTILITIES

At ---Fort Revere,--Mass.

Date June 30, 1941.

[illegible]

RECORD OF EQUIPMENT AND CONDITION OF UTILITIES

At Fort Revere, Mass.

Date June 30, 1941

RAILROADS	CONNECTING RAILROAD AT POST		TRACK GAUGE	WEIGHT OF RAIL	KIND OF RAIL	MAINTAINED BY--	GOVERNMENT OWNED		RAILROAD OWNED		TOTAL TURNOUTS	TOTAL MILES TRACK
	MILES TRACK	TURNOUTS	MILES TRACK	TURNOUTS								
	None											

WHARVES	POST BLDG. No.	MATERIALS					DIMENSIONS		ELEVATION OF DECK		DEPTH OF MEAN LOW WATER	DIFFICULTIES IN MAINTAINING AND REPAIRING WHARF	REPAIRS MADE	
		SUBSTRUCTURE	DECK	SUPER-STRUCTURE	BACKFILL	TREATED OR UNTREATED	WHARF	APPROACH	H. W.	L. W.			KIND	DATE
		None												

TARGET RANGES	LOCATION _____ AREA _____ GOVERNMENT OWNED _____ LEASED _____										
	CONDITION	TARGETS INSTALLED		RANGE YARDS	TARGETS		BUTTS		TRENCH		FACILITIES
		No.	TYPE		WIDTH	INTERVAL	WIDTH	LENGTH	WIDTH	HOW DRAINED	
	Good	4	Ind cors-22 & 45 caliber	50 ft.							

BOILER AND POWER PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT	REFRIGERATING PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT
			None		None		

WATER PUMPING PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT	HEATING	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT

SEWAGE PUMPING PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT	HEATING	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT

FENCES	RESERVATION			INTERIOR		
	CONDITION	KIND	LENGTH	CONDITION	KIND	LENGTH
	Good	Chain link wire	6735' 1.3 mi.		None	

INSTRUCTIONS.—This report will be prepared annually as directed in paragraph 8, A. R. 30-1770.
 Under the heading "Extensions, additions, alterations, or replacements" any changes that have been made in the equipment of the utility referred to during the present fiscal year will be reported. Opposite "Heating" report changes in the square feet of radiation installed in buildings or boilers in individual heating plants. If there have been no additions or alterations statement to that effect will be made.

RECORD OF EQUIPMENT AND CONDITION OF UTILITIES

At Fort Revere, Mass.

Date June 30, 1940

POST NAME OF STREET OR ROAD	ROADS				WALKS				CONDITION	EXTENSIONS OR ALTERATIONS			
	KIND	LENGTH MILES OR FEET	WIDTH FEET	CONDITION	KIND	LENGTH MILES OR FEET	WIDTH FEET	CONDITION		KIND	DIAM.	LENGTH	REMARKS
	Macadam	1 ¹ / ₂ miles	16'	Poor	Concrete	3/4 Mile	5	Fair					
									WATER MAINS	Fair			
									DRAINAGE	Fair			
									SEWER MAINS	Fair Replacement of Sewer Main. \$3462.32			
									GAS MAINS	None	None		
									ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT				
									WATER TREATMENT PLANTS	None			
									SEWAGE TREATMENT PLANTS	None			
									ELECTRICAL EQUIPMENT	Installed 13 Poles Nov 28, 1939			
	TOTAL	1 ¹ / ₂ miles			TOTAL	3/4 mile							

RECORD OF EQUIPMENT AND CONDITION OF UTILITIES

At Port Revere, Mass.

Date June 30, 1940

RAILROADS	CONNECTING RAILROAD AT POST		TRACK GAUGE	WEIGHT OF RAIL	KIND OF RAIL	MAINTAINED BY—	GOVERNMENT OWNED		RAILROAD OWNED		TOTAL TURNOUTS	TOTAL MILES TRACK
	MILES TRACK	TURNOUTS	MILES TRACK	TURNOUTS								
	None											

WHARVES	POST BLDG. No.	MATERIALS					DIMENSIONS		ELEVATION OF DECK		DEPTH OF MEAN LOW WATER	DIFFICULTIES IN MAINTAINING AND REPAIRING WHARF	REPAIRS MADE	
		SUBSTRUCTURE	DECK	SUPER-STRUCTURE	BACKFILL	TREATED OR UNTREATED	WHARF	APPROACH	H. W.	L. W.			KIND	DATE
		None												

TARGET RANGES	LOCATION		AREA		GOVERNMENT OWNED		LEASED					
	CONDITION	No.	TARGETS INSTALLED		RANGE YARDS	TARGETS		BUTTS		TRENCH		FACILITIES
			Type	WIDTH		INTERVAL	WIDTH	LENGTH	WIDTH	HOW DRAINED		
	None											Water connections Sewer connections Telephone Electric lights

BOILER AND POWER PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT	REFRIGERATING PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT
			None		None		

WATER PUMPING PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT	HEATING	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT

SEWAGE PUMPING PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT	HEATING	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT

FENCES	RESERVATION			INTERIOR		
	CONDITION	KIND	LENGTH	CONDITION	KIND	LENGTH
	Good	Chain link wire	6785'		None	

INSTRUCTIONS.—This report will be prepared annually as directed in paragraph 8, A. R. 30-1770.

Under the heading "Extensions, additions, alterations, or replacements" any changes that have been made in the equipment of the utility referred to during the present fiscal year will be reported. Opposite "Heating" report changes in the square feet of radiation installed in buildings or boilers in individual heating plants. If there have been no additions or alterations statement to that effect will be made.

RECORD OF EQUIPMENT AND CONDITION OF UTILITIES

At Fort Revere, Mass.

Date June 30, 1939

[illegible]

RECORD OF EQUIPMENT AND CONDITION OF UTILITIES

Date June 30, 1939

At Fort Revere, Mass.

RAILROADS	CONNECTING RAILROAD AT POST		TRACK GAUGE	WEIGHT OF RAIL	KIND OF RAIL	MAINTAINED BY—	GOVERNMENT OWNED		RAILROAD OWNED		TOTAL TURNOUTS	TOTAL MILES TRACK
	None						MILES TRACK	TURNOUTS	MILES TRACK	TURNOUTS		

WHARVES	POST BLDG. No.	MATERIALS					DIMENSIONS		ELEVATION OF DECK		DEPTH OF MEAN LOW WATER	DIFFICULTIES IN MAINTAINING AND REPAIRING WHARF	REPAIRS MADE		
		SUBSTRUCTURE	DECK	SUPER-STRUCTURE	BACKFILL	TREATED OR UNTREATED	WHARF	APPROACH	H. W.	L. W.			KIND	DATE	
		None													

TARGET RANGES	AREA										GOVERNMENT OWNED		LEASED	
	LOCATION		TARGETS INSTALLED			RANGE YARDS	TARGETS		BUTTS		TRENCH		FACILITIES	
	CONDITION	No.	TYPE	WIDTH	INTERVAL		WIDTH	LENGTH	WIDTH	HOW DRAINED				
						None								

BOILER AND POWER PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT	REFRIGERATING PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT

WATER PUMPING PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT	HEATING	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT

SEWAGE PUMPING PLANTS	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT	HEATING	IN BLDG. No.	CONDITION	ADDITIONS, ALTERATIONS, OR REPLACEMENTS IN EQUIPMENT

FENCES	RESERVATION			INTERIOR		
	CONDITION	KIND	LENGTH	CONDITION	KIND	LENGTH

INSTRUCTIONS.—This report will be prepared annually as directed in paragraph 8, A. R. 30-1770. Under the heading "Extensions, additions, alterations, or replacements" any changes that have been made in the equipment of the utility referred to during the present fiscal year will be reported. Opposite "Heating" report changes in the square feet of radiation installed in buildings or boilers in individual heating plants. If there have been no additions or alterations statement to that effect will be made.

FURNITURE

FORT REVERE, MASS.

[illegible]

REFRIGERATORS AND LOCKERS

[illegible]

ELECTRIC LIGHTING AND POWER

At Fort Revere, Mass.

Date December 31, 1939

1. Post generating plant, active or inactive ----- Original cost -----
Date completed ----- Total capacity -----
2. If purchased, give name and address of contracting firm Town of Hull Elec. Light Co.,
Nantasket Beach, Mass.
3. Incoming lines at reservation boundary: Voltage 2300 Phase 1
Frequency 60 Number of conductors 2 Aerial or underground Aerial
Length of line from contractor's plant or substation, in miles 3 1/2 or feet -----
4. Service lines from reservation boundary to substation: Owner U.S. Gov't.
Length, in miles ----- or feet 50 Aerial or underground Aerial
Number of: Poles 1 Manholes ----- Height of poles 30 How treated creolin
Kind of: Poles Pine Manholes ----- Duct -----
5. Substation: Original cost ----- Date completed -----
Type of construction outside switch house in metal housing. Dimensions -----
Main transformer bank: Owner -----
Quantity ----- Manufacturer -----
Name-plate data -----
Mounted outdoor or indoor ----- Connection of windings: Primary Multiple Secondary Multiple
Lightning arresters: Quantity ----- Manufacturer -----
Name-plate data -----
Where and how mounted -----
Switchboard: Material Slate Dimensions 1'4" x 4' x 1'3/4"
Number of panels 1 Number of oil breakers 1 Number of air switches -----
List of instruments 1 GE master meter, type I, 10 Amp, 2300 V; 1 GE current transformer; 1 GE potential transformer, type G; & 1 oil switch, GE, 150 Amp, 2500 Volt.
Number of circuits leaving station 1 Aerial or underground Aerial
Voltage regulators: Quantity ----- Manufacturer -----
Name-plate data -----
Street-lighting regulators: Quantity ----- Manufacturer -----
Name-plate data -----
Other Government-owned apparatus -----
Apparatus owned by contractor, including metering facilities -----

6. Distribution system: Original cost Date completed

Aerial or underground Aerial Phase 1 Number of conductors 2

Voltage: Primary 2300 Secondary: Power 110 Light 110

Length, in miles 2 1/4 or feet --- Number of poles 15 Kind of poles Pine & Chestnut

Number of: Cross arms 39 Insulators 90 Manholes ---

Kind of: Cross arms Pine Insulators Glass

Kind of: Manholes --- Duct lines 1

Number of lightning arresters --- Type --- Manufacturer ---

Number of distribution transformers in service 2 Aggregate K. V. A. 15

Method of mounting transformers On poles

Method of grounding arresters, tanks and neutral Grounded to water pipe in bldgs.

7. Exterior lighting system: Original cost --- Date completed ---

Series or multiple Series Voltage or amperage 6.6

Number of lamps 16 Wattage or lumens 100

B. & S. gage of conductors 8 Length of system 1/2 mile

Type of fixtures Cast Iron, Standard How mounted Concrete bases

8. Interior installations: Lighting, total kilowatts connected 6.12

Ranges: Total kilowatts connected --- Number installed ---

Water heaters: Total kilowatts connected --- Number installed ---

Air heaters: Total kilowatts connected --- Number installed ---

Fans: Number of A. C. installed --- Number of D. C. installed ---

Motors: A. C., total horsepower connected --- Number installed ---

Motors: D. C., total horsepower connected --- Number installed ---

List miscellaneous Government-owned apparatus, giving group designations, total quantities, and total kilowatt ratings: ---

Privately owned appliances: Total kilowatts connected (estimated) 3 KW

Enter pertinent information on motors, except desk and bracket fans on reverse side of this sheet.

9. This space for use of O. Q. M. G.

INSTRUCTIONS.—This form is for permanent record and will be used when new systems or extensive additions are completed and turned over for use.

It will be prepared in triplicate. One copy of each form will be retained at the station where prepared, one copy will be forwarded to the Department or Corps Area Commander, and one copy (the original) will be forwarded to the Quartermaster General. At independent stations, forms will be prepared in duplicate, one copy will be retained at the station and the original will be forwarded to the Quartermaster General.

Slight modifications, alterations, or additions will be promptly reported to the Quartermaster General giving all particulars with notation as to how such modifications were made. It is not necessary to submit new forms when reporting such slight modifications, etc. Inasmuch as these forms are used to check upon the electric system in operation, entries hereon will be checked annually, or oftener, if necessary, and reported for correction. Entries hereon will be considered accurate at all times.

TRANSFORMERS

3-9642

Date December 31, 1939

[illegible]

3-0041

[illegible]

WATER-SUPPLY SYSTEM

At Fort Revere, Mass.

Date January 24, 1930

Source of water supply Purchased from Town of Hingham, Mass.
Sanitary conditions surrounding source of supply Good

Quality of water Good

Has the capacity of the supply been fully developed? Not known

Describe distribution system Pressure, Metropolitan Pumping Plant

3-9773

FILTRATION				SOFTENER			CHEMICAL FEED AND STERILIZING EQUIPMENT					
	SEDIMENTATION BASIN	FILTERS	CLEAR-WATER BASIN		SOFTENER TANKS	BRINE TANKS	CHLORINATORS					
							NUMBER	CAPACITY	MAKE	TYPE	COST	DATE INSTALLED
Number	None	None	None	Make	None	None	None	None	None	None	None	None
Dimensions				No. units								
Material				Dimensions			DRY FEED MACHINES					
Capacity				Capacity			NUMBER	CHEM. USED	CAPACITY	MAKE	HOW DRIVEN	COST
Cost				Material			None	None	None	None	None	None
Date installed				Cost			SOLUTION FEED EQUIPMENT					
Type				Date installed			NUMBER	SIZE TANKS	CHEMICAL USED	HOW CONTROLLED	COST	Date Installed
Bldg. No.				Building No.			None	None	None	None	None	None
				Kind of zeolite								
				Capacity per regeneration		Kilograms						

WELLS								WATER METERS						
NO. OF WELL	KIND	DEPTH	DIAM.	MANNER PUMPED	CAPACITY, - G. P. M.	COST	DATE INSTALLED	WATER LEVEL		NUMBER	MAKE	TYPE	SIZE	BUILDING NO.
								Standing	Draw Down					
None	None	None	None	None	None	None	None	None	None	1	Hersey	Disk	6"	None

WATER MAINS								WATER ANALYSIS												
MATERIAL		DIAM.	LENGTH	SOURCE SUPPLY	CLASS	COST	DATE INSTALLED	Date of analysis	Total hardness (as CaCO ₃)	Alkalinity to methyl orange (as CaCO ₃)	Hydrogen ion concentration (pH)	Total iron	Magnesium	Calcium	Sulphates (as SO ₄)	Chlorides (as Cl)	Sodium and Potassium (as Na)	Average Color	Average Turbidity	Parts per Million
Mains	Joint																			
Cast Iron Lead		4"	800'	Metropolitan	A	Unknown	Unknown	11/12/29												15
" "	and	6"	2400'	Pumping	A	"	"	Where made at												
" "	oakum	8"	962'	Plant	A	"	"	State Laboratory, Boston, Mass.												.140
			4162					Where collected at												
								tap in Town												
								Hingham, Mass.												6.80

As of 7/31/41:
Mains - 4" & over - 1.35 mi.
Pipe - under 4" - .5 "
Total 1.85 mi.

TANKS, RESERVOIRS, CISTERNS, ETC.										PRESSURE		
BUILDING NO.	MATERIAL	DIMENSIONS	SOURCE SUPPLY	CAPACITY, GALLONS	TRESTLE		ELEV. HIGH WATER		COST	DATE INSTALLED	AT HIGHEST FIRE HYDRANT	AT LOWEST FIRE HYDRANT
					Height	Material	Pump	Flagpole				
18	Concrete	50' x 20'	Metropolitan	117,504	Water Tower		None	50'	12012.00	6/12/03	40	40
			Pumping									
			Plant									

Number fire hydrants 20
Standpipes for sprinkling carts (number):
None

SEWERAGE SYSTEM

At Fort Revere, Mass.

Date January 22, 1930.

[illegible]

Means of disposal of sewage Discharges into Town of Hull Sewer

[illegible]

SEWAGE-TREATMENT PLANT

	SCREENING AND DETRITUS CHAMBER	SEWAGE TANKS	FILTERS	SLUDGE BEDS	SECONDARY SEDIMENTATION TANKS	CONTACT BEDS	INTERMITTENT SAND FILTERS	CHLORINATING APPARATUS
Number,	None	None	None	None	None	None	None	None
Dimensions,								
Drawing Nos.,								
Cost,								
Date installed,								
Remarks:								

INCINERATORS

[illegible]

SEWERAGE SYSTEM—CONTINUED

.0891

FLUSH TANKS					GREASE TRAPS					SEWAGE EJECTORS				
UNIT NO.	NAME OF MANUFACTURER	SIZE	DATE INSTALLED	COST	UNIT NO.	NAME OF MANUFACTURER	SIZE	DATE INSTALLED	COST	UNIT NO.	NAME OF MANUFACTURER	SIZE	DATE INSTALLED	COST
None	None	None	None	None	None	None	None	None	None	None	None	None	None	None

INSTRUCTIONS

Sewers and Drainage.—Under material, state whether vitrified clay, cast iron, brick, concrete, or ditch, etc. In case of ditches, give width and depth instead of diameter.

Means of Disposal of Sewage.—State whether the outfall sewer discharges into ocean, lake, stream, city sewer, or sewage-treatment plant.

Centrifugal Pumps—Unit Number.—Give number used by the utilities officer on his records of the apparatus referred to.

Building Number.—Give number of building where pump is installed.

How driven.—Motor, gas engine, or steam.

Total head, capacity, and R. P. M.—Take these items from name-plate data.

Operating Conditions—Suction Lift.—Give suction lift under which pump is operating.

Discharge head.—Give total head under which pump is operating. This includes static plus friction head.

This form is for permanent record and will be used only when new installations are made, or extensive alterations or additions are first completed and turned over for use.

Forms will be prepared in triplicate. One copy of each form will be retained at the station where prepared, one copy will be forwarded to the Department or Corps Area Commander, and one copy (the original) will be forwarded to the Quartermaster General. At independent stations forms will be prepared only in duplicate, one copy for retention at the station, and the other for submission to the Quartermaster General.

Slight modifications, alterations, or additions will be reported promptly upon completion of the work to the Quartermaster General, as directed in par. 7, AR 30-1770.

At Fort Revere, Mass.

Date January 21, 1930

U. S. GOVERNMENT PRINTING OFFICE: 1979 3-9772

CENTRIFUGAL, TURBINE, AND DIRECT-ACTING PUMPS

[illegible]

AIR-LIFT PUMPS

[illegible]

AIR COMPRESSORS

[illegible]

Remarks:

FIRE PROTECTION

At Fort Revere, Mass.

Date May 10, 1922.

FIRE DEPARTMENT ORGANIZATION

NO. OF STATION	NO. MEN EACH STATION	NO. OF STATION	NO. MEN EACH STATION
None			
Total		Total	

Remarks: No fire stations. 1 Fire apparatus house.

OUTSIDE AID.

LOCATION	DISTANCE	TIME
Fire Department, Town of Hull, Mass.	500 yds	5 Min

Remarks: Modern fire fighting apparatus available from Town of Hull, Mass.,
within 5 minutes after alarm is turned in.

WATER SUPPLY.

		PRESSURE IN MAINS	
		Due to tanks or reservoirs	Direct pumping
Capacity of tanks	117504 Gal		
Capacity of reservoirs.....	750	80	Max. 85
Capacity pump, max. G. P. M.....	24hrs. Constant 25000 gal.	60	Min. 60
Duration of water supply			

Remarks:

AUTOMATIC SPRINKLER SYSTEMS.

[illegible]

Remarks:

STANDPIPE SYSTEMS.

Designation and number of buildings equipped	None
--	------

Remarks:

HOSE CONNECTIONS AT PLUGS

	POST	NEAREST TOWN
Number of threads per inch.....	9	9
Diameter of male couplings over threads.....	3 ¹¹	3 ¹¹

Remarks:

FIRE-ALARM SYSTEMS

[illegible]

Remarks: Fire call by musician of the Guard. Telephone Hull fire dept.

FIRE-FIGHTING APPARATUS

Capacity, G. P. M.	Name of Manufacturer	Number
Triple comb'n pumping engines.....	None	
Double comb'n chem'l and hose trucks.....	None	
Hook and ladder truck.....	One	56
Utilities car.....	None	
Wheel-type chemical extinguishers.....	None	
Hose carts, hand-drawn.....	Combination Ladder Co	1
1-quart extinguishers.....	Providence, R.I.	
2½-gallon soda-and-acid extinguishers.....		
2½-gallon foam-type extinguishers.....		
5-gallon hand pump tank.....	Segrave, C. Columbus, O.	35
Hose—2½-inch, double jacket.....	1200	
2½-inch, single jacket.....	None	
Unlined linen.....	None	
Other apparatus:	fire buckets	56

Remarks: Fire Hazard "Very Good"

INDIVIDUAL HEATING PLANTS

At Fort Revere, Mass.

3-9639

Date June 30, 1938.

[illegible]

(SEE OTHER SIDE)

RECORD OF EQUIPMENT AND CONDITION OF BUILDINGS

Date June 30, 1941

Reservation—Area 75.065 acres.

Name Fort Revere Location Hull, Massachusetts Established 1900 Government-owned 75.065 acres. Leased 0 acres.

Character of post Coast Artillery Telegraph station Hingham, Massachusetts 512 Tents Freight station Nantasket, Massachusetts

Capacity: Officers 27 2 MP 25 BE; N. C. O. 4 P; Enl. men 1142 630 E; Animals 3; Motor veh. 10 ?; Hosp. beds 0 Infirmary

POST BLDG. No.	DESIGNATION OF BUILDING	Laundry Stoves	HOT-WATER HEATERS					Range Boilers	RANGES OR COOKERS					METERS					Toilets	Urinals	Kitchen Sinks	Washbasins	Laundry Tubs	Shower Baths	Bathtubs	Fire Extinguishers	Fire Buckets	Storm Windows	Screens	Designed Capacity	Present Occupancy	REMARKS ON CONDITION OF BUILDINGS
			Coal	Oil	Gas	Steam	Electric		Coal	Oil	Gas	Steam	Electric	Water	Gas	Oil	Steam	Electric														
	Housing																															
	A. Enlisted Men																															
	(1) Family Type																															
	(a) Permanent																															
✓ 15 & 15A	NCO Quarters																											2F	0	Fair		
✓ 16 & 16A	NCO Quarters																											2F	8P	Fair		
	(2) Barrack Type																															
	(c) Emergency																															
✓ T-9	Barracks																											63P	29	Good		
✓ T-10	Barracks																											63P	43	Good		
✓ T-14	Barracks																											63P	43	Good		
✓ T-15	Barracks																											63P	42	Good		
✓ T-17	Barracks																											63P	45	Good		
✓ T-18	Barracks																											63P	45	Good		
✓ T-19	Barracks																											63P	40	Good		
✓ T-20	Barracks																											63P	44	Good		
✓ T-24	Barracks																											63P	45	Good		
✓ T-25	Barracks																											63P	45	Good		
	B. Officers																											630				
	(1) Family Type																															
	(a) Permanent																															
✓ 2&2A	Officers Qtrs																											2F	0	Good		
	(c) Emergency																															
✓ T-2	Officers Qtrs																											25	18	Good		
	C. Mess Hall																															
	(c) Emergency																															
✓ T-13	Mess Hall																											179P		Good		
✓ T-21	Mess Hall																											179P		Good		
✓ T-22	Mess Hall																											179P		Good		
✓ T-23	Mess Hall																											179P		Good		
	D. Storage																															
	(a) Permanent																															
✓ 10	Ord. Storeroom																											2252	sq ft	Good		
✓ 19	QM Storehouse																											6885	sq ft	Good		
✓ 43	A.E. Storehouse																											707	sq ft	Good		
	(c) Emergency																															
✓ T-6	Storehouse																											2056	sq ft	Good		
✓ T-7	Storehouse																											2056	sq ft	Good		
	H. All other type																															
	(a) Permanent																															
✓ 11	Bakery																											1	Oven	Fair		
✓ 13	Guard House																											2P		Fair		

RECORD OF EQUIPMENT AND CONDITION OF BUILDINGS

NAME OF POST FORT REVERE

DATE June 30, 1941

POST BLDG. No.	DESIGNATION OF BUILDING	Laundry Stoves	HOT-WATER HEATERS					Range Boilers	RANGES OR COOKERS					METERS					Toilets	Urinals	Kitchen Sinks	Washbasins	Laundry Tubs	Shower Baths	Bathtubs	Fire Extinguishers	Fire Buckets	Storm Windows	Screens	Designed Capacity	Present Occupancy	REMARKS ON CONDITION OF BUILDINGS
			Coal	Oil	Gas	Steam	Electric		Coal	Oil	Gas	Steam	Electric	Water	Gas	Oil	Steam	Electric														
✓*22	Searchlight Shed																														3 Animals	Good
✓✓44	Reservation Fence																														6785 lin ft	Good
✓✓18	Water Tower																														117504 Gal	Good
	(c) Emergency																															
✓T-1	Theatre																														357P	Good
✓T-3	Day Room																														1570 sq ft	Good
✓T-4	Infirmary																														2234 sq.ft.	Good
✓T-5	Day Room																														1148 sq ft	Good
✓T-8	Co. Adm. Bldg.	(2)																													2461 sq.ft.	Good
✓T-11	Fire House																														2000 sq.ft.	Good
✓T-12	Post Exchange																														2331 sq.ft.	Good
✓T-16	Co. Adm. Bldg.	(2)																													2461 sq.ft.	Good
✓T-26	Day Room																														1087 sq ft	Good
✓T-27	Day Room																														1087 sq ft	Good
✓T-28	Day Room																														1087 sq ft	Good
	I. Tent Frames																															
	(c) Emergency																															
	Tent Frames	(64)																													512P	Good
	*At present being used as a stable.																															

16-5780

INSTRUCTIONS.—Preamble, opposite "Capacity" give total number that can be accommodated in all the buildings at the post available for the purpose indicated.

In each column headed "Laundry Stoves," "Ranges," etc., give number installed in the building indicated.

Ranges: Indicate separate meter for cooking or heating by placing star (*) after number of ranges.

In column headed "Capacity" give capacity of building in accordance with the instructions for the preparation of Historical Records, Form 117 (Old Form 173 a).

Place Fort Revere, Mass
 Designation of building Single Officer's Qrs.; Capacity Captain
 Total cost \$ 8874.50; Date completed 11-8-02
 Material: Walls Frame; Foundation Stone
 Roof Slate; Floors Wood
 Total floor area above basement, square feet 4256
 Dimensions of main building 32' x 36'; Wings 20' x 22'
 EACH AND EVERY ROOM ARRANGED BY FLOORS.

Basement
 1R-32'6"x35'5" 1R-7'2"x7'9" 1R-10'7"x11'9"
First Floor
 1R-4'10"x15'8" 1R-14'10"x18'
 1R-6'x10' 10'8"x17'8" 1Hall-4'3"x19'9"
 1R-10'11"x15'2" 1R-11'10"x12'10" 1R-8'x8'10"
Second Floor
 1R-12'10"x16'2" 1R-13'2"x18'1R-6'8"x8'
 1R-11'10"x12'10" 1R-10'11"x13'2" 2Cl-3'6"x5'6"
 2R-5'10"x8' 1Cl-3'6"x6' 1H-10'8"x17'8"
 1H-4'3"x16'6" 1Cl-2'x9'9"
Attic
 1R-36'x52'

PROVIDED WITH:
 Heating Steam
 (---400---sq. ft. rad.)
 Lighting Electricity
 Water connections Yes
 Sewer " "
 Water-closets, No. 2
 Urinals, No. 2
 Wash sinks, No. 2
 Washbasins, No. 2
 Laundry tubs, No. 2
 Shower baths, No. 2
 Bathtubs, No. 2
 Screens, No. Yes
 Storm sash, No. Yes
 " doors, No. Yes
 Window shades, No. Yes

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

O. Q. M. G.: Plan No. 143 Building No. 1



(Formerly numbered 3.)

HEAVY FURNITURE INSTALLED.	REPAIRS.
<u>To Mch. 1, 1912</u>	Expended to 3-1-09. <u>\$772.52</u>
Bedsteads, iron	Year ending 3-1-10. <u>\$ 74.50</u>
Bookcases <u>1</u>	" " 3-1-11. <u>3.50</u>
Chairs, dining, arm <u>2</u> <u>Mahog.</u>	" " 3-1-12. <u>100.00</u>
" " side <u>6</u>	" " 3-1-13. <u>356.62</u>
" library, arm <u>1</u>	" " 3-1-14. <u>245.25</u>
" " side <u>1</u>	" " 3-1-15. <u>102.44</u>
Chests of drawers <u>2</u>	" " 3-1-16. <u>30.11</u>
Curtain poles <u>1</u>	" " 3-1-17. <u>54.92</u>
Desks <u>1</u>	" " 3-1-18. <u>131.70</u>
Divans	" " 3-1-19. <u>329.00</u>
Hat racks	" " 3-1-20. <u>329.00</u>
Refrigerators <u>1</u>	" " 3-1-21. <u>329.00</u>
Sideboards <u>1</u>	" " 3-1-22. <u>329.00</u>
Tables, dining <u>1</u>	" " 3-1-23. <u>329.00</u>
" kitchen <u>1</u>	" " 3-1-24. <u>329.00</u>
" parlor <u>1</u>	" " 3-1-25. <u>329.00</u>
Wall lockers	" " 3-1-26. <u>329.00</u>
	Total <u>\$ 329.00</u>

Building No. 2 O. Q. M. G.: Plan No. 120-A

HEAVY FURNITURE INSTALLED.

REPAIRS.

To <u>Mc.h.1, 1912, Each half:</u>	Expended to 3-1-09	\$ <u>986.83</u>
Bedsteads, iron	Year ending 3-1-10	\$ <u>150.25</u>
Bookcases <u>1</u>	" " 3-1-11	<u>10.60</u>
Chairs, dining, arm <u>2</u> <u>Mahog.</u>	" " 3-1-12	<u>108.00</u>
" " side <u>6</u>	" " 3-1-13	
" library, arm <u>1</u>	" " 3-1-14	<u>258.17</u>
" " side	" " 3-1-15	<u>450.75</u>
Chests of drawers <u>1</u>	" " 3-1-16	<u>172.89</u>
Curtain poles	" " 3-1-17	<u>90.97</u>
Desks <u>1</u>	" " 3-1-18	<u>402.64</u>
Divans	" " 3-1-19	<u>193.10</u>
Hat racks	" " 3-1-20	
Refrigerators <u>1</u>	" " 3-1-21	<u>498.20</u>
Sideboards	" " 3-1-22	
Tables, dining <u>1</u>	" " 3-1-23	
" kitchen <u>1</u>	" " 3-1-24	
" parlor <u>1</u>	" " 3-1-25	
Wall lockers	" " 3-1-26	
	Total	\$

Place Fort Revere, Mass.

Designation of building Double Officers' Quarters; Capacity 1-2 Lieuts.

Total cost, \$ 11492.00; Date completed 11-8-02

Material: Walls Frame; Foundation Stone

Roof Slate; Floors Wood

Total floor area above basement, square feet. 5001

Dimensions of main building 32' x 55'; Wings 13' x 13'

PROVIDED WITH:

Heating Steam

(600 sq. ft. rad.)

Lighting Electricity

Water connections Yes

Sewer "

Water-closets, No. 4

Urinals, No. 4

Wash sinks, No. 4

Washbasins, No. 2

Laundry tubs, No. 4

Shower baths, No. 2

Bathtubs, No. 2

Screens, No. Yes

Storm sash, No. "

" doors, No. "

Window shades, No. "

EACH AND EVERY ROOM ARRANGED BY FLOORS.

Basement

2R-12'7"x16'2" 2R-12'6"x16'4" 2R-12'2"x14'10" 2C1-5'4"x6'7" 2H-5'5"x6'10" 2R-10'2"x11'

First Floor

2R-13'6"x16'4" 2R-12'6"x15'10" 2H-14'6"x13'8" 2H-5'2"x12'1" 2C1-5'7"x8' 2R-12'1"x12'2"

Second Floor

2R-13'6"x16'8" 2R-12'4"x12'6" 2C1-3'1"x3'4" 2H-3'1"x3'2" 2C1-3'x3' 2C1-6'6"x9'6" 2H-3'8"x19'5" 2H-7'6"x9'6" 2R-5'7"x9'6" 2R-12'1"x12'2" 2H-2'6"x9'6"

Attic

2R-28'x32' 1R-13'9"x15'

Constructed Mc.h.6/06 1R-14'8"x13'7"

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.



O. Q. M. G.: Plan No. 92-B Building No. 9

EACH AND EVERY ROOM ARRANGED BY FLOORS.

PROVIDED WITH:

1R-14' x 20'

Heating -----
(-----sq. ft. rad.)-----
Lighting -----
Water connections -----
Sewer " -----
Water-closets, No. -----
Urinals, No. -----
Wash sinks, No. -----
Washbasins, No. -----
Laundry tubs, No. -----
Shower baths, No. -----
Bathtubs, No. -----
Screens, No. -----
Storm sash, No. -----
" doors, No. -----
Window shades, No. -----



HEAVY FURNITURE INSTALLED.

REPAIRS.

Expended to 3-1-09 \$ 8.80

- Year ending 3-1-10- \$-----

Bedsteads, iron -----	Year ending 3-1-10. \$-----
-----------------------	-----------------------------

Bookcases _____ " " 3-I-II- _____

Chairs, dining, arm -----	"	"	3-I-12..	<u>12.00</u>
---------------------------	---	---	----------	--------------

“ “ side 3-I-13-

“ library, arm -----	“ “ 3-I-14- -11.00
----------------------	--------------------

“ “ side _____ “ “ 3-1-15- _____

Chests of drawers ----- " " 3-I-16-----

Curtain poles ----- " " 3-I-17-----

Desks 3-I-18

Divans " " 6-30-88 10-26500

Tracks	3-1-20-
--------	---------

Refrigerators ----- " " 6-30-
1-1-21 80.00

Sideboards	“	“	3-I-22
------------	---	---	--------

Tables, dining	"	"	3-I-23
----------------	---	---	--------

" kitchen 3-I-25-

" parlor _____ " " 3-I-25 _____

Wall lockers	3-I-26
--------------	--------

Total ----- \$-----

Q. M. C. Form No. 173 a.
Authorized November 15, 1913.

24c

Building No. 10 O. Q. M. G.: Plan No. 137-A

HEAVY FURNITURE INSTALLED.

REPAIRS.

	Expended to 3-1-09.	\$ 265.00
	Year ending 3-1-10.	\$ 23.00
Bedsteads, iron	" " 3-1-11.	
Bookcases	" " 3-1-12.	130.00
Chairs, dining, arm	" " 3-1-13.	
" " side	" " 3-1-14.	50.00
" library, arm	" " 3-1-15.	57.75
" " side	" " 3-1-16.	47.56
Chests of drawers	" " 3-1-17.	15.00
Curtain poles	" " 3-1-18.	106.54
Desks	" " 3-1-19.	14.63
Divans	" " 3-1-20.	
Hatracks	" " 3-1-21.	100.00
Refrigerators	" " 3-1-22.	
Sideboards	" " 3-1-23.	
Tables, dining	" " 3-1-24.	
" kitchen	" " 3-1-25.	
" parlor	" " 3-1-26.	
Wall lockers		
	Total	\$

Place Fort Revere, Mass.
 Designation of building Gymnasium Ordinance Storehouse; Capacity 7000 cu. ft.
 Total cost, \$ 2800.00; Date completed 9-25-02
 Material: Walls Wood; Foundation Brick
 Roof Slate; Floors Wood
 Total floor area above basement, square feet 2250
 Dimensions of main building 30' x 75'; Wings
 PROVIDED WITH: EACH AND EVERY ROOM ARRANGED BY FLOORS.
 Heating Stove (sq. ft. rad.)
 Lighting Min. Oil
 Water connections
 Sewer
 Water-closets, No.
 Urinals, No.
 Wash sinks, No.
 Washbasins, No.
 Laundry tubs, No.
 Shower baths, No.
 Bathtubs, No.
 Screens, No.
 Storm sash, No.
 " doors, No.
 Window shades, No.


First Floor

1R-29'10"x65'2" 2R-11' x 14'

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

This building was formerly designated "Ordinance Storehouse".
 Jan. 26, 1915 it was changed into a Gymnasium. (\$600.911)
 1922 Designated as Ordinance Storehouse

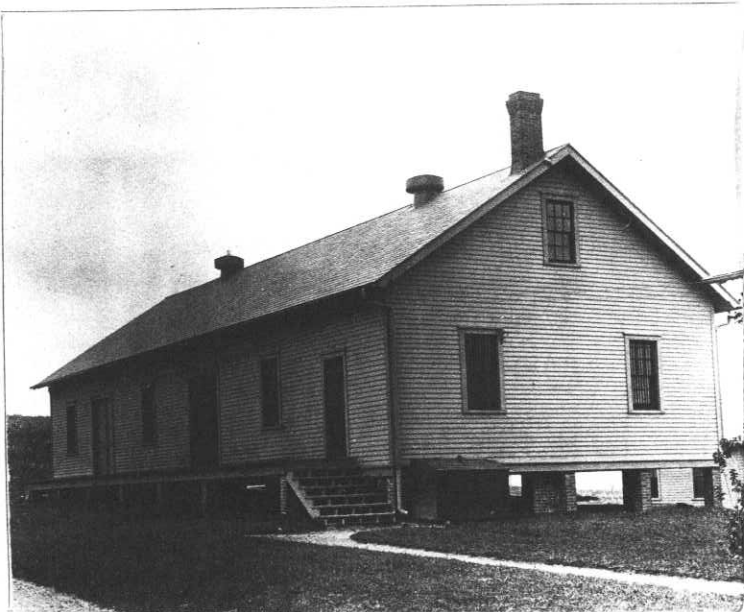

Place Fort Revere, Mass.

O. Q. M. G.: Plan No. 49-D

Building No. 11

Designation of building Pake House; Capacity 1 Pake Oven

Total cost, \$ 2530.00; Date completed 9-25-02

Material: Walls Wood; Foundation Brick

Roof Slate; Floors Wood & Concrete

Total floor area above basement, square feet 908

Dimensions of main building 22' x 44'; Wings

EACH AND EVERY ROOM ARRANGED BY FLOORS.

PROVIDED WITH:

Heating Stove

(sq. ft. rad.)

Lighting Min Oil

Water connections Yes

Sewer " "

Water-closets, No.

Urinals, No.

Wash sinks, No. 1

Washbasins, No.

Laundry tubs, No.

Shower baths, No.

Bathtubs, No.

Screens, No. Yes

Storm sash, No. "

" doors, No. "

Window shades, No.



HEAVY FURNITURE INSTALLED.

REPAIRS.

	Expended to 3-1-09. \$ <u>254.00</u>
Bedsteads, iron	Year ending 3-1-10. \$ <u>16.70</u>
Bookcases	" " 3-1-11. <u> </u>
Chairs, dining, arm	" " 3-1-12. <u>80.00</u>
" " side	" " 3-1-13. <u> </u>
" library, arm	" " 3-1-14. <u>51.00</u>
" " side	" " 3-1-15. <u>116.25</u>
Chests of drawers	" " 3-1-16. <u> </u>
Curtain poles	" " 3-1-17. <u> </u>
Desks	" " 3-1-18. <u>35.48</u>
Divans	" " 3-1-19. <u>72.70</u>
Hatracks	" " 3-1-20. <u> </u>
Refrigerators	" " 3-1-21. <u>123.00</u>
Sideboards	" " 3-1-22. <u> </u>
Tables, dining	" " 3-1-23. <u> </u>
" kitchen	" " 3-1-24. <u> </u>
" parlor	" " 3-1-25. <u> </u>
Wall lockers	" " 3-1-26. <u> </u>
Total	\$ <u> </u>

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

The floor in one half of this building is concrete.

Building No. 12 O. Q. M. G.: Plan No. 1-26: Special Place Fort Revere, Mass.

HEAVY FURNITURE INSTALLED.

REPAIRS.

	Expended to 3-1-09	\$ 448.42
Bedsteads, iron	Year ending 3-1-10	\$ 82.50
Bookcases	" " 3-1-11	38.10
Chairs, dining, arm	" " 3-1-12	102.00
" " side	" " 3-1-13	122.00
" library, arm	" " 3-1-14	124.50
" " side	" " 3-1-15	22.36
Chests of drawers	" " 3-1-16	85.64
Curtain poles	" " 3-1-17	90.83
Desks	" " 3-1-18	
Divans	" " 3-1-19	
Hat racks	" " 3-1-20	
Refrigerators	" " 3-1-21	371.20
Sideboards	" " 3-1-22	
Tables, dining	" " 3-1-23	
" kitchen	" " 3-1-24	
" parlor	" " 3-1-25	
Wall lockers	" " 3-1-26	
	Total	\$

Designation of building Admin. P. Exchange Post Tel. Shop, Teamsters Qrs.; Capacity
 Switchboard R. Tailor Shop, Teamsters Qrs.
 Total cost, \$-6300.00; Date completed 2-25-01

Material: Walls Wood; Foundation Brick
 Roof Wood; Floors Wood
 Total floor area above basement, square feet 3629

Dimensions of main building 24' x 104'; Wings 20' x 55'

PROVIDED WITH:

EACH AND EVERY ROOM ARRANGED BY FLOORS.

Heating Stoves
 (sq. ft. rad.)
 Lighting Electricity
 Water connections Yes
 Sewer " "
 Water-closets, No.
 Urinals, No.
 Wash sinks, No.
 Washbasins, No.
 Laundry tubs, No.
 Shower baths, No.
 Bathtubs, No.
 Screens, No. For part of bldg.
 Storm sash, No. Yes
 " doors, No. "
 Window shades, No.

1R-11'10"x23' 1R-12'x23' 1R-23'1"x
 36'6" 1R-19'x23'9" 1R-23'1"x28'8"
 1R-11'10"x23'1" 1R-11'5"x13'6" 1R-19'x
 19'6" 1R-15'x19'

Salvage Nov 30 1937


ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

This building was formerly termed "Temporary Barracks", later it was called "Administration, Post Ex. & Gym. Bldg." A sound proof wall was constructed between the Hdqrs. Office & Gym. No cost. Post labor. Material from demolished bldg. Material, Wood & Plaster. To Mch. 1/08 Electric light fixtures installed, cost-\$142.00

The part of bldg. occupied by Post Exchange provided with Screens, cost-\$154.72
 To Mch. 1/09 Alteration- 1 room 10'3"x 23'2" partitioned off for use, Tel. Exchange 4/30/08. No cost. Post labor. Material from demolished bldg. Construction of Toilet room 6'3"x10'6" 4/30/08. No cost, as above.

Installation of 2 water closets and 1 lavatory 4/30/08. Cost-\$219.50

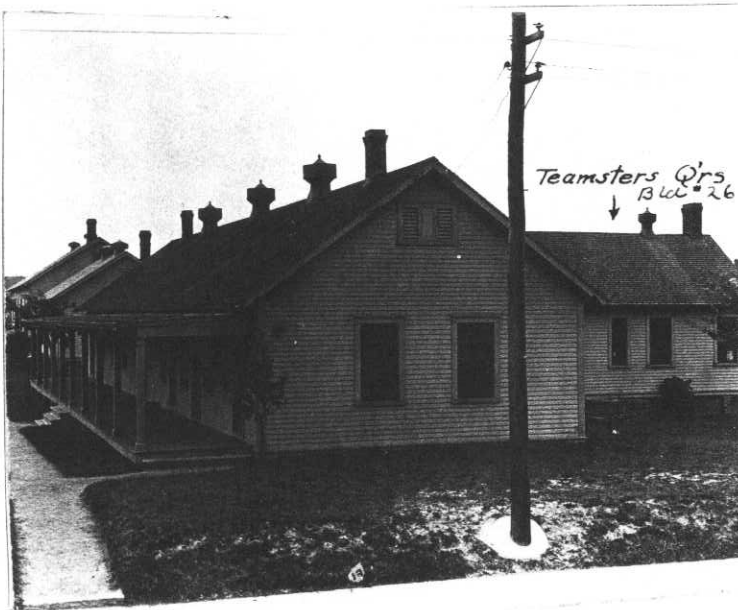

134, 72
 142, 00

O. Q. M. G.: Plan No. 30-B Building No. 13

PROVIDED WITH:

Heating ----- **Stoves** -----
(-----sq. ft. rad.)

Lighting ----- **Min.Oil** -----

Water connections ----- **Yes** -----

Sewer " ----- **"** -----

Water-closets, No. ----- **2** -----

Urinals, No. ----- **2** -----

Wash sinks, No. -----

Washbasins, No. ----- **2** -----

Laundry tubs, No. -----

Shower baths, No. -----

Bathtubs, No. -----

Screens, No. ----- **Yes** -----

Storm sash, No. ----- **"** -----

" doors, No. ----- **"** -----

Window shades, No. -----

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

A black and white photograph of a small, single-story wooden house with a gabled roof and a prominent chimney. The house has a front porch supported by columns and a set of steps leading up to it. A street lamp is visible in the foreground on the left.

REPAIRS.

	Expended to 3-1-09.	\$	127.50
Bedsteads, iron	Year ending 3-1-10.	\$	49.00
Bookcases	" " 3-1-11.		8.65
Chairs, dining, arm	" " 3-1-12.		85.00
" " side	" " 3-1-13.		
" library, arm	" " 3-1-14.		128.00
" " side	" " 3-1-15.		78.75
Chests of drawers	" " 3-1-16.		.25
Curtain poles	" " 3-1-17.		85.75
Desks	" " 3-1-18.		66.84
Divans	" " 3-1-19.		93.08
Hat racks	" " 3-1-20.		
Refrigerators	" " 3-1-21.		36.00
Sideboards	" " 3-1-22.		
Tables, dining	" " 3-1-23.		
" kitchen	" " 3-1-24.		
" parlor	" " 3-1-25.		
Wall lockers	" " 3-1-26.		
	Total	\$	

Building No. 14 O. Q. M. G.: Plan No. 121-E

Place Fort Revere, Mass.

Designation of building Artillery Barracks; Capacity 100 men

Total cost, \$ 27965.00; Date completed 11-8-02

Material: Walls Frame; Foundation Stone

Roof Slate; Floors Wood

Total floor area above basement, square feet 14872

Dimensions of main building 26' x 122'; Wings (2) 26' x 45'

PROVIDED WITH:

EACH AND EVERY ROOM ARRANGED BY FLOORS.

Basement

1R-22'6"x43'4" 1R-22'6"x45'10"

1R-25' x 47'6" 1R-21'x35'4"

First Floor

2R-11'11"x16'9" 1R-31'6"x24'6" 1H-10'7"

x22' 1H-12'6"x16'11" 1R-9'4"x 13'

1R-6'3"x9'4" 1R-8'x10'6" 1R-9'x16'3"

1R-24'6"x48'9" 1R-24'6"x44'4" 1H-6'x20'11"

1R-8'x8'9" 1R-24'x24'6"

Second Floor

2R-48'9"x74'6" 1R-9'x10'9" 1H-5'x23'

2R-10'7"x10'9"

Attic

1R-24'x121'10" & 2 wings 24'x45'

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

63 lockers were removed from buildings #14 & 15 at Fort Warren, Mass. and 28 from building #15 at Fort Banks, Mass. (total 91) and installed in this building. Approved by the Sec'y of War Nov. 25, 1913. #485289, the 105 lockers previously installed in this bldg. having been transferred to Ft. Strong, Mass. in May 1911.

8th Ind. dated Nov. 23, 1925 - Bath tubs (4) and partitions in latrine of barrack building removed.

HEAVY FURNITURE INSTALLED.	REPAIRS.
	Expended to 3-1-09 \$ <u>1653.77</u>
Bedsteads, iron	Year ending 3-1-10 \$ <u>440.75</u>
Bookcases	" " 3-1-11 <u>12.51</u>
Chairs, dining, arm	" " 3-1-12 <u>450.00</u>
" " side	" " 3-1-13
" library, arm	" " 3-1-14 <u>1251.88</u>
" " side	" " 3-1-15 <u>732.75</u>
Chests of drawers	" " 3-1-16 <u>100.35</u>
Curtain poles	" " 3-1-17 <u>330.51</u>
Desks	" " 3-1-18 <u>386.74</u>
Divans	" " 3-1-19 <u>422.46</u>
Hatracks	" " 3-1-20
Refrigerators	" " 6-30-21 <u>1246.00</u>
Sideboards	" " 3-1-22
Tables, dining	" " 3-1-23
" kitchen	" " 3-1-24
" parlor	" " 3-1-25
Wall lockers <u>91</u>	" " 3-1-26
	Total \$



O. Q. M. G.: Plan No. 82-E Building No. 15

PROVIDED WITH:

A black and white photograph of a two-story wooden house with a gambrel roof, two chimneys, and a front porch. The house is surrounded by a lawn and some shrubbery.

ADDITIONS AND INSTALLATIONS.

Ventilators cut in first and second floors ,each set, to aid in heating. Authority not known.

HEAVY FURNITURE INSTALLED.

To Mch. 1, 1912

REPAIRS.

Expended to 3-1-09	\$ 323.60
--------------------	-----------

			Year ending	3-1-10.	\$	91.00
Bedsteads, iron			"	"	3-1-11.	10.00
Bookcases			"	"	3-1-12.	90.00
Chairs, dining, arm			"	"	3-1-13.	
" " side			"	"	3-1-14.	108.00
" library, arm			"	"	3-1-15.	189.75
" " side			"	"	3-1-16.	77.37
Chests of drawers			"	"	3-1-17.	63.33
Curtain poles			"	"	3-1-18.	77.87
Desks			"	"	3-1-19.	101.66
Divans			"	"	3-1-20.	
Hat racks			"	"	3-1-21.	212.00
Refrigerators	1	1	"	"	3-1-22.	
Sideboards			"	"	3-1-23.	
Tables, dining			"	"	3-1-24.	
" kitchen			"	"	3-1-25.	
" parlor			"	"	3-1-26.	
Wall lockers			"	"		

Total _____ \$_____

Building No. 16 O. Q. M. G.: Plan No. 82-E

HEAVY FURNITURE INSTALLED:		REPAIRS.	
To <u>Mar 1, 1912</u>		Expended to 3-1-09	\$340.95
Bedsteads, iron		Year ending 3-1-10	\$85.00
Bookcases		" " 3-1-11	10.00
Chairs, dining, arm		" " 3-1-12	90.00
" " side		" " 3-1-13	
" library, arm		" " 3-1-14	108.00
" " side		" " 3-1-15	189.75
Chests of drawers		" " 3-1-16	78.87
Curtain poles		" " 3-1-17	43.58
Desks		" " 3-1-18	112.59
Divans		" " 3-1-19	117.74
Hat racks		" " 3-1-20	
Refrigerators	1 1	" " 3-1-21	219.00
Sideboards		" " 3-1-22	
Tables, dining		" " 3-1-23	
" kitchen		" " 3-1-24	
" parlor		" " 3-1-25	
Wall lockers		" " 3-1-26	
		Total	\$

Place Fort Revere, Mass.

Designation of building Double N.C.S.Qrs.; Capacity 2N.C.S.O.

Total cost, \$ 5664.00; Date completed 10-7-02

Material: Walls Frame; Foundation Stone

Roof Slate; Floors Wood

Total floor area above basement, square feet 1682

Dimensions of main building 27' x 28'; Wings

PROVIDED WITH:

EACH AND EVERY ROOM ARRANGED BY FLOORS.

Heating Steam

(sq. ft. rad.)

Lighting Min. oil

Water connections Yes

Sewer " "

Water-closets, No. 2

Urinals, No. 2

Wash sinks, No. 2

Washbasins, No. 2

Laundry tubs, No. 2

Shower baths, No. 2

Bathtubs, No. 2

Screens, No. Yes

Storm sash, No. "

" doors, No. "

Window shades, No. "

Basement

2R-14'1"x24'4"

First Floor

2R-11'1"x14'8" 2R-10'10"x17'5"

2H-5'10"x14'8"

Second Floor

2R-5'10"x 7' 2R-11'1"x 14'8"

2R-10'10"x11'1" 2H-5'10"x9'2"

2C1-4'8"x5'10" 2C1-2'4"x3'8"

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

Ventilators cut in the first and second floors, each set, to aid in heating.



1R-20'10"x21'8"	1R-20'10"x21'7"
2R-10'x13'4"	

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

Salvaged - 5-15-28

A black and white photograph of a two-story wooden building with a corrugated metal roof and a tall, dark chimney on the left side. The building has several windows and a door, and is surrounded by trees and foliage.

Q. M. C. Form No. 173 a.
Authorized November 15, 1913.

Building No. 18 O. Q. M. G.: Plan No. 8 Hennebigue

Place Fort Revere, Mass.

HEAVY FURNITURE INSTALLED.	REPAIRS.
	Expended to 3-1-09. \$
	Year ending 3-1-10. \$
Bedsteads, iron	" " 3-1-11.
Bookcases	" " 3-1-12.
Chairs, dining, arm	" " 3-1-13.
" " side	" " 3-1-14. <u>35.00</u>
" library, arm	" " 3-1-15. <u>1.50</u>
" " side	" " 3-1-16.
Chests of drawers	" " 3-1-17. <u>5.00</u>
Curtain poles	" " 3-1-18.
Desks	" " 3-1-19. <u>33.16</u>
Divans	" " 3-1-20.
Hatracks	" " 6.12 21. <u>70.00</u>
Refrigerators	" " 3-1-22.
Sideboards	" " 3-1-23.
Tables, dining	" " 3-1-24.
" kitchen	" " 3-1-25.
" parlor	" " 3-1-26.
Wall lockers	Total \$

Designation of building Water Tower; Capacity 117,500 gal.
Total cost, \$ 12012.00; Date completed 6-12-03

Material: Walls Concrete; Foundation Concrete

Roof Slate; Floors Concrete

Total floor area above basement, square feet

Dimensions of main building Ht. 88' D. 30'; Wings

PROVIDED WITH:

EACH AND EVERY ROOM ARRANGED BY FLOORS.

Heating

(sq. ft. rad.)

Lighting

Water connections

Sewer

Water-closets, No.

Urinals, No.

Wash sinks, No.

Washbasins, No.

Laundry tubs, No.

Shower baths, No.

Bathtubs, No.

Screens, No.

Storm sash, No.


" doors, No.

Window shades, No.

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

Cylindrical tank 20' in diameter, 50' in height.

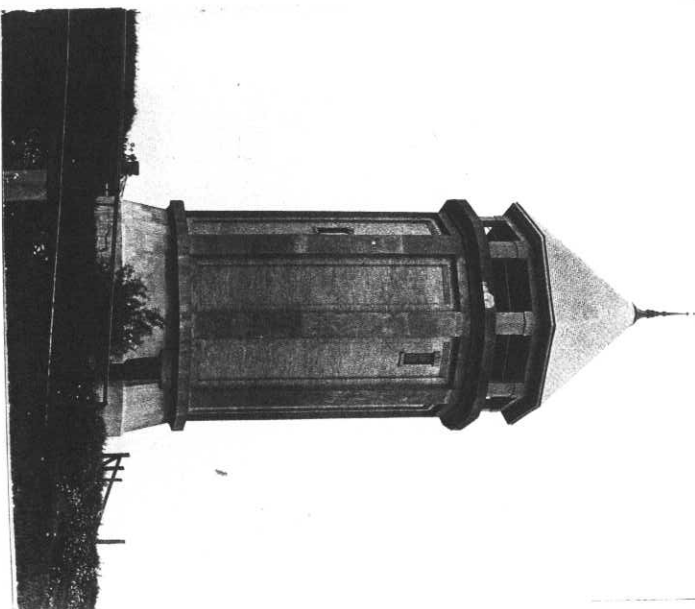

Place Fort Revere, Mass.Designation of building Q.M. Engr. & Ordnance Storehouse; Capacity as indicatedTotal cost, \$ 14,352.76; Date completed 3-28-06Material: Walls Brick; Foundation StoneRoof Slate; Floors WoodTotal floor area above basement, square feet 6885Dimensions of main building 32' x 120'; Wings

EACH AND EVERY ROOM ARRANGED BY FLOORS.

PROVIDED WITH:

Heating Steam(680 sq. ft. rad.)Lighting Min. oilWater connections YesSewer "Water-closets, No. "Urinals, No. "Wash sinks, No. "Washbasins, No. 1Laundry tubs, No. "Shower baths, No. "Bathtubs, No. "Screens, No. "Storm sash, No. "" doors, No. "Window shades, No. "

Basement

1R-29' x 59' 8" 1R-29' x 38' 1"1R-29' x 17' 7"

First Floor

1R-29' 10" x 25' 1R-29' 10" x 20' 6" 1R-19' 9"x 14' 1R-9' 7" x 14' 1R-19' 9" x 19' 9" 1R-9' 7"x 14' 1R-29' 10" x 36' 2" 1R-9' 7" x 5' 3"

Second Floor

1R-29' 10" x 59' 6" 1R-29' 10" x 55' 11"

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.


Change in original plan made by changing door on north side of Q.M. Storeroom to window.

To Mch. 1/09 Construction of 1 Toilet room 7' x 9' 5" June 8/08

Cost in connection with installation and Sewer connection \$740.00

Installation of 1 Water Closet and 1 Lavatory 6/8/08. Cost in above.

10' x 16' Refrigerator built in basement.

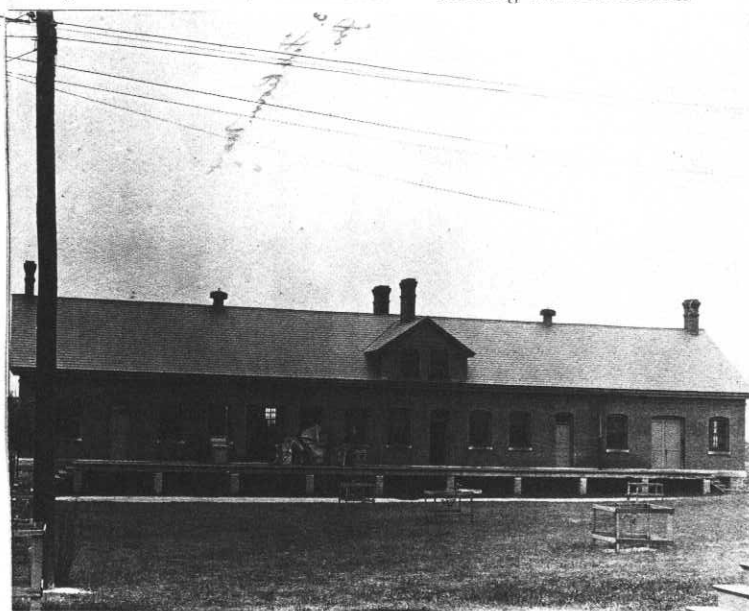O. Q. M. G.: Plan No. 91-DBuilding No. 19

HEAVY FURNITURE INSTALLED.

REPAIRS.

	Expended to 3-1-09- \$ <u>175.80</u>
	Year ending 3-1-10- \$ <u>62.00</u>
Bedsteads, iron	" " 3-1-11- <u>6.50</u>
Bookcases	" " 3-1-12- <u>23.50</u>
Chairs, dining, arm	" " 3-1-13- <u>40.00</u>
" " side	" " 3-1-14- <u>116.25</u>
" " library, arm	" " 3-1-15- <u>30.00</u>
" " side	" " 3-1-16- <u>17.42</u>
Chests of drawers	" " 3-1-17- <u>121.57</u>
Curtain poles	" " 3-1-18- <u>51.00</u>
Desks	" " 3-1-19- <u>98.00</u>
Divans	" " 3-1-20- <u>30.00</u>
Hatracks	" " 3-1-21- <u>98.00</u>
Refrigerators <u>1</u>	" " 3-1-22- <u>30.00</u>
Sideboards	" " 3-1-23- <u>30.00</u>
Tables, dining	" " 3-1-24- <u>30.00</u>
" kitchen	" " 3-1-25- <u>30.00</u>
" parlor	" " 3-1-26- <u>30.00</u>
Wall lockers	" " 3-1-26- <u>30.00</u>
	Total \$ <u>98.00</u>

Building No. 20 O. Q. M. G.: Plan No. 60-II


HEAVY FURNITURE INSTALLED.	REPAIRS.
	Expended to 3-1-09 \$ <u>170.00</u>
Bedsteads, iron	Year ending 3-1-10 \$ <u>13.00</u>
Bookcases	" " 3-1-11 <u>4.00</u>
Chairs, dining, arm	" " 3-1-12 <u>15.00</u>
" " side	" " 3-1-13 <u>8.00</u>
" library, arm	" " 3-1-14 <u>7.50</u>
" " side	" " 3-1-15
Chests of drawers	" " 3-1-16
Curtain poles	" " 3-1-17
Desks	" " 3-1-18
Divans	" " 3-1-19
Hatracks	" " 3-1-20
Refrigerators	" " 3-1-21
Sideboards	" " 3-1-22
Tables, dining	" " 3-1-23
" kitchen	" " 3-1-24
" parlor	" " 3-1-25
Wall lockers	" " 3-1-26
	Total \$

Place Fort Revere, Mass.
Designation of building Wagon Shed; Capacity 10 Vehicles
Total cost, \$ 1,745.00; Date completed 3-28-06
Material: Walls Wood; Foundation Stone
Roof Slate; Floors Gravel
Total floor area above basement, square feet 1915
Dimensions of main building 30'x54'10"; Wings
PROVIDED WITH: EACH AND EVERY ROOM ARRANGED BY FLOORS.
Heating (sq. ft. rad.)
Lighting 1R-30' x 45'5" 1R-30' x 12'5"
Water connections
Sewer
Water-closets, No.
Urinals, No.
Wash sinks, No.
Washbasins, No.
Laundry tubs, No.
Shower baths, No.
Bathtubs, No.
Screens, No.
Storm sash, No.
" doors, No.
Window shades, No.

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

February 2, 1924 - Wagon Shed destroyed by fire.

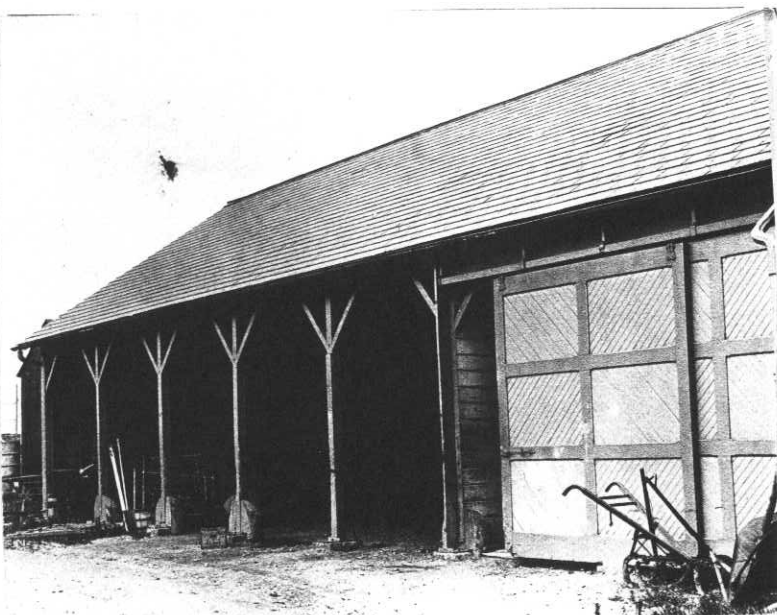

Building No. 22 O. Q. M. G.: Plan No. 167

HEAVY FURNITURE INSTALLED.	REPAIRS.
	Expended to 3-1-09. \$
	Year ending 3-1-10. \$
Bedsteads, iron	" " 3-1-11. "
Bookcases	" " 3-1-12. "
Chairs, dining, arm	" " 3-1-13. "
" " side	" " 3-1-14. "
" library, arm	" " 3-1-15. <u>3.25</u>
" " side	" " 3-1-16. "
Chests of drawers	" " 3-1-17. "
Curtain poles	" " 3-1-18. "
Desks	" " 3-1-19. <u>40.70</u>
Divans	" " 3-1-20. "
Hatracks	" " 3-1-21. <u>20.00</u>
Refrigerators	" " 3-1-22. "
Sideboards	" " 3-1-23. "
Tables, dining	" " 3-1-24. "
" kitchen	" " 3-1-25. "
" parlor	" " 3-1-26. "
Wall lockers	Total \$

Place Fort Revere, Mass. Soughlight Shed Used as stable
 Designation of building Shelter, Sch. Light Truck; Capacity as indicated.
 Total cost, \$ 761.00; Date completed 7-31-06
 Material: Walls Galv. Iron; Foundation Concrete
 Roof Galv. Iron; Floors Gravel
 Total floor area above basement, square feet 474
 Dimensions of main building 18' x 28'; Wings

PROVIDED WITH: EACH AND EVERY ROOM ARRANGED BY FLOORS.

Heating
 (sq. ft. rad.)
 Lighting
 Water connections
 Sewer
 Water-closets, No.
 Urinals, No.
 Wash sinks, No.
 Washbasins, No.
 Laundry tubs, No.
 Shower baths, No.
 Bathtubs, No.
 Screens, No.
 Storm sash, No.
 " doors, No.
 Window shades, No.

1R-17'4"x27'4"

ADDITIONS AND INSTALLATIONS.

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

1917 Designation changed to Oil House
 2nd IND 600.911 OQM Ft Revere 7-27-22

February 23, 1945 - Building salvaged



Building No. 26

O. Q. M. G.: Plan No.

HEAVY FURNITURE INSTALLED	REPAIRS
Bedsteads, iron, single	Expended to 6-30-21 \$ 109.80
“ “ double	
Bookcases	Year ending 6-30-22 \$
Chairs, dining, arm	“ “ 6-30-23
“ “ side	“ “ 6-30-24
“ library, arm	“ “ 6-30-25
“ “ side	“ “ 6-30-26
Chests of drawers	“ “ 6-30-27
Curtain poles	“ “ 6-30-28
Desks	“ “ 6-30-29
Dressers	“ “ 6-30-30
Davenport	“ “ 6-30-31
Hat racks	“ “ 6-30-32
Refrigerators	“ “ 6-30-33
Rocking chairs	“ “ 6-30-34
Sideboards	“ “ 6-30-35
Tables, dining	“ “ 6-30-36
“ kitchen	“ “ 6-30-37
“ library	“ “ 6-30-38
“ parlor	“ “ 6-30-39
Wall lockers	“ “ 6-30-40
	Total



Place	Fort Revere, Massachusetts.		
Designation of building	Teamsters Quarters	Capacity	2 men
Total cost, \$	-	Date completed	-
Material: Walls	Wood	Foundation	Concrete Pillars
Roof	Paper	Floors	Wood
Total floor area above basement, square feet	262		
Size: Main building	14'5" x 20'4"	Wings	Basement

PROVIDED WITH—

How heated	Stove
(..... sq. ft. rad.)	
How lighted	Electricity
Water connections	Yes
Sewer connections	Yes
Gas connections	
Water-closets, No.	
Urinals, No.	
Wash sinks, No.	1
Washbasins, No.	
Laundry tubs, No.	
Shower baths, No.	
Bathtubs, No.	
Screens, No.	
Storm sash, No.	
Storm doors, No.	
Window shades, No.	
Ranges	Coal, No.
	Gas, No.
	Electric, No.
Meters	Water, No.
	Gas, No.
	Electric, No.

SIZE OF ROOMS

[illegible]

ADDITIONS AND INSTALLATIONS

Below enter chronologically all modifications, additions, introductions of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

Building left at post by Engineer Department. Moved to site of Quartermaster Stables by post labor. Rear of Bldg # 12

EACH AND EVERY ROOM ARRANGED BY FLOORS.

1st Floor

1 - Room -	- 11' x 15'
1 - Room -	- 4' x 12'
1 - Room -	- 5' 6" x 11'
1 - Hall -	- 6' x 3'

2nd Floor

1 - Room -	- 12' x 16'
1 - Room -	- 14' x 16'

Below enter chronologically all modifications, additions, introduction of water, sewer, lights, etc., also dates for all changes of listed articles, etc.

A black and white photograph of a two-story brick building. A wide staircase with a metal railing leads from the ground level to a small platform in front of a second-floor door. To the left of the door is a window. The building is situated on a grassy slope. The photograph is framed by a white border.

HEAVY FURNITURE INSTALLED.	REPAIRS.	
-----	Expended to 3-1-09	\$-----
Bedsteads, iron -----	Year ending 3-1-10	\$-----
Bookcases -----	" " 3-1-11	-----
Chairs, dining, arm -----	" " 3-1-12	-----
" " side -----	" " 3-1-13	-----
" library, arm -----	" " 3-1-14	-----
" " side -----	" " 3-1-15	-----
Chests of drawers -----	" " 3-1-16	-----
Curtain poles -----	" " 3-1-17	-----
Desks -----	" " 3-1-18	-----
Divans -----	" " 3-1-19	-----
Hatracks -----	" " 3-1-20	-----
Refrigerators -----	" " 3-1-21	-----
Sideboards -----	" " 3-1-22	-----
Tables, dining -----	" " 3-1-23	-----
" kitchen -----	" " 3-1-24	-----
" parlor -----	" " 3-1-25	-----
Wall lockers -----	" " 3-1-26	-----
-----	Total -----	\$-----

Post Plan No. None

O.Q.M.G.: Plan No. _____ Name _____ Building No. 44

Place Fort Revere, Mass.
Designation of building Reservation Fence Capacity ---
Total cost, \$ \$9992.15 Date completed January 20, 1939
Material: ~~WALL~~ Chain link Foundation Concrete
Roof --- Floors ---
Total floor area above basement, square feet ---
Size: ~~Main building~~ 6785 L. ft. ~~Wing~~ Height 6 ft. Basement ---
a --- Height of first floor above ground ---
(How heated)
b --- How lighted ---
(Type of heat)
Water connections ---
c --- Sewer connections ---
(Type of domestic hot water heater) Gas connections ---

COOKING RANGES INSTALLED
(Give quantity and size)

Energy Source	Percentage (%)
Coal	10
Gas	15
Electric	20
Oil	35
Steam	20

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas _____
Electric _____
Ice _____

METERS INSTALLED
[(Give quantity and capacity)]

Energy Source	Percentage of Total Energy Consumption
Gas	22.0%
Electric	18.0%
Oil	35.0%
Steam	15.0%
Water	9.0%



ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.O.M.G.: Plan No. 700-310 Building No. T-1

Place Fort Revere, Hull, Massachusetts
Designation of building Recreation Building Capacity 364
Total cost, \$ 12,193.00 Date completed August 25, 1941
Material: Walls Wood Foundation **Concrete
Roof Prepared roofing on ***Wood Floors *Concrete - wood
Total floor area above basement, square feet 3663 sq. ft. plus Proj. Rm. 91 Sq. Ft.
Size: Main building 99'x37' approx 22'-6" Wings None Basement None
a Indiv. heating system (Low heated) Height of first floor above ground 12"
b Forced warm air (Type of heat) How lighted Electric
Water connections 3/4"
c None (Type of domestic hot water heater) Sewer connections 4"
Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED

(Give quantity and size)

Gas _____ None _____

Electric _____ None _____

Ice _____ None _____


METERS INSTALLED

(Give quantity and capacity)	
Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

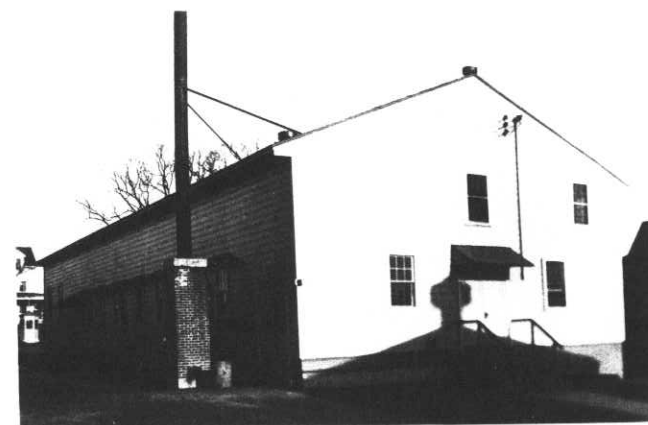[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.

"b" State whether steam, vapor, hot water, or hot air.

"c" State whether gas, coal, oil, or central heating plant.

Post Plan No. None

O.Q.M.G.: Plan No. 700-1254 Building No. T-2

Place Fort Revere, Hull, Mass.
Designation of building Officers' Quarters & Mess. Capacity 25
Total cost, \$ 15,565.00 Date completed August 25, 1941
Material: Walls Wood Foundation **Concrete
Roof Weed & prepared roofing, on Wead Floors *Wood-concrete
Total floor area above basement, square feet 2,650 sq. ft.
Size: Main building 106'x29'-6" Wings None Basement None
a Indiv. Htg. System Height of first floor above ground 1'
(How heated)
b Forced Warm Air How lighted Electric
(Type of heat)
c Coal Water connections 2"
(Type of domestic hot water heater) Sewer connections 6"
Gas connections 2"

COOKING RANGES INSTALLED
(Give quantity and size)

Coal 1-#5 Army
Gas None
Electric 1-Deep Fat Fryer
Oil None
Steam "

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas ----- None
Electric ----- "
Ice ----- 1-#6


METERS INSTALLED
(Give quantity and capacity)

Gas	None
Electric	"
Oil	"
Steam	"
Water	"

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

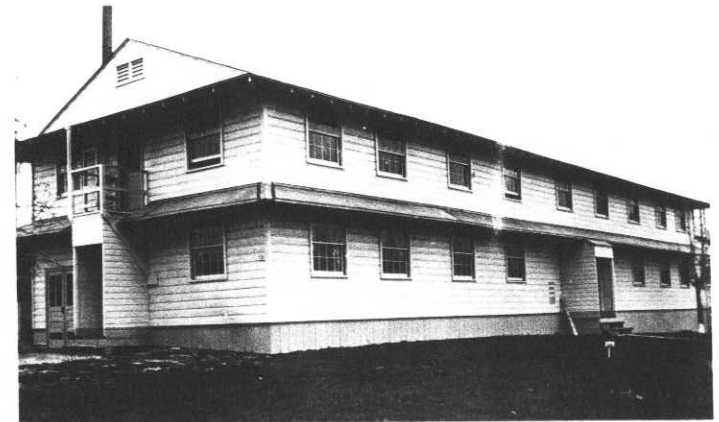
[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.

"b" State whether steam, vapor, hot water, or hot air.

"c" State whether gas, coal, oil, or central heating plant.

See reverse side of form.

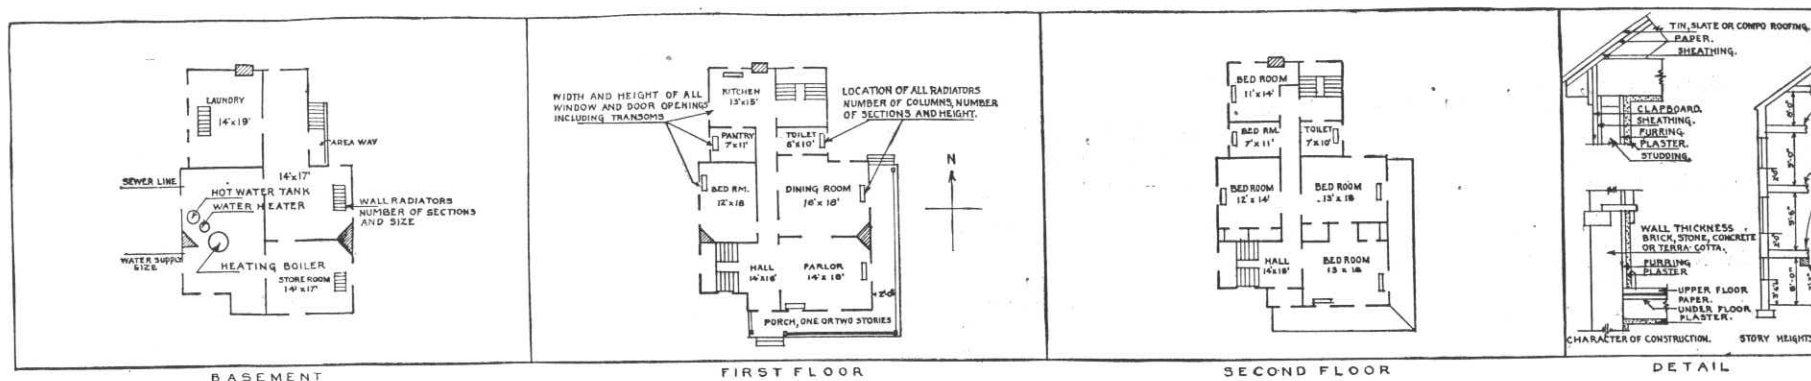

IN SPACE BELOW SKETCH BASEMENT AND FLOOR PLANS OF BUILDINGS, GIVING DATA AS PER PLANS ABOVE

REMARKS

*Floor in heater room is concrete-other floors 2 1/4" matched flooring.

**Concrete piers with the exception of the area of the heating room, which has concrete foundation walls.

Note: For building plan see ~~DWG~~ Drawing #700-1254.

INSTRUCTIONS

If plans of building are available, forward copy of same showing information called for above. These plans should be checked against the building and any variations from same in the building as constructed should be noted.

If plans are not available make sketch plans and elevation in spaces above. The plans shown are typical of "quarters." Similar plans may be made for all types of buildings. There are 10 squares to the inch. Each square will represent 1', 2', 4', or 8', etc., as may be necessary to show entire building in the space allowed. Show inside dimensions and designation of each room. Indicate location of water and sewer connections. In space under heading "Details" show character of construction, story heights, etc.

Post Plan No. None

O.Q.M.G.: Plan No. 800-210 Building No. T-3

Place Fort Revere, Hull, Massachusetts
Designation of building Administration Building Capacity 10 Desks
Total cost, \$ 5,074.00 Date completed August 25, 1941
Material: Walls Wood Foundation **Concrete
Roof Wood & prepared roofing on Wood Floors Wood & *concrete
Total floor area above basement, square feet 1575 sq. ft.
Size: Main building 63'-2" x 25'4" Wings None Basement None
a Indiv. htg. system approx. 14' high Height of first floor above ground 12"
(How heated)
b Forced warm air How lighted Electric
(Type of heat)
Water connections 12"
c None Sewer connections 6"
(Type of domestic hot water heater)
Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas _____ None _____
Electric _____ None _____
Ice _____ None _____

METERS INSTALLED
(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.O.M.G.: Plan No. 800-1443 Building No. T-4

Place Fort Revere, Hull Massachusetts
Designation of building Infirmary Capacity 21 beds
Total cost, \$ 7280.00 Date completed August 25, 1941
Material: Walls Wood Foundation *Concrete
Roof Prepared roofing on wood Floors **Wood & concrete
Total floor area above basement, square feet 2250 sq. ft.
Size: Main building 90'-2"x25'-4" Wings None Basement None
a Individual heating system Height of first floor above
(How heated) ground 1'
b Forced Warm Air How lighted Electric
(Type of heat) Water connections 1 1/2"
c Coal Sewer connections 4"
(Type of domestic hot water heater) Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED

(Give quantity and size)

Gas _____ None _____

Electric _____ None _____

Ice _____ None _____

METERS INSTALLED

(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.



Post Plan No. None

O.Q.M.G.: Plan No. 800-459 Building No. T-5

Place Fort Revere, Massachusetts
Designation of building Recreation Building A-5 Capacity 100-Men
Total cost, \$ 3795.00 Date completed August 25, 1941
Material: Walls Wood Foundation ** Concrete
Roof wood and prepared roofing on Wood Floors * Concrete and wood
Total floor area above basement, square feet 1120
Size: Main building 45'-2" x 25'-4" Wings NONE Basement NONE
a Indiv. Htg. system (approx. 14') Height of first floor above ground 12"
b Forced Warm air (Type of heat) How lighted Electric
None (Type of domestic hot water heater) Water connections None
c Sewer connections "
Gas connections "

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	"
Electric	"
Oil	"
Steam	"

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas	None
Electric	"
Ice	"


METERS INSTALLED
(Give quantity and capacity)

Gas	None
Electric	"
Oil	"
Steam	"
Water	"

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

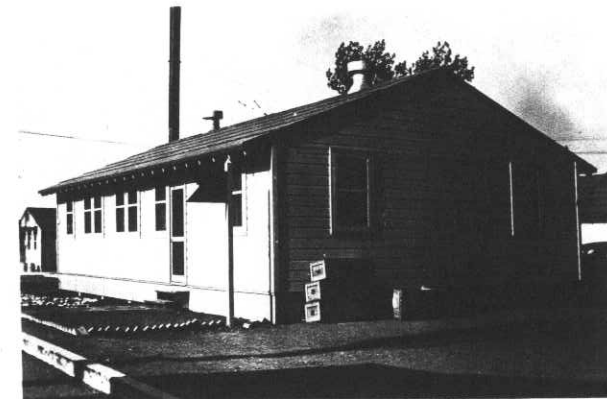[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 800-664 Building No. T-6

Place Fort Revere, Hull, Mass.
Designation of building Storehouse Capacity 21,600 Cu. Ft.
Total cost, \$ 4635.00 Date completed September 25, 1941
Material: Walls Wood Foundation Concrete
Roof Wood & Prepared Roofing on Wood Floors Concrete
Total floor area above basement, square feet 2700 sq. ft.
Size: Main building 108'-2" x 251' x 4" Wings None Basement None
a None Height of first floor above ground 1'
(How heated)
b None How lighted Electric
(Type of heat)
Water connections None
c None Sewer connections None
(Type of domestic hot water heater)
Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED

(Give quantity and size)

Gas None

Electric None

Ice None

METERS INSTALLED


(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

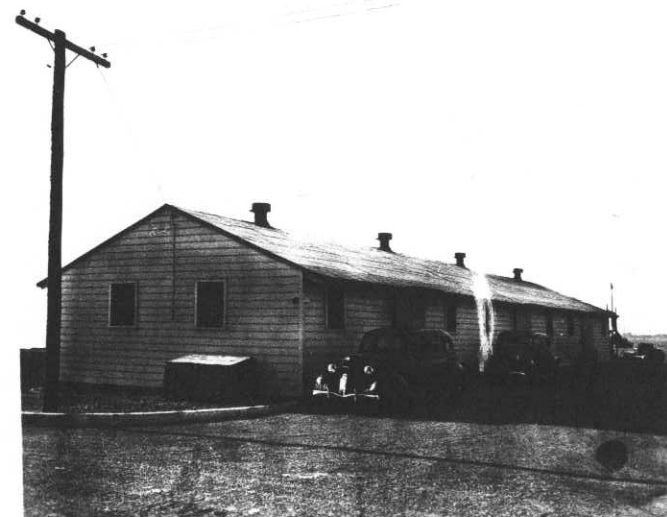[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 800-663 Building No. T-7

Place Fort Revere, Hull, Massachusetts
Designation of building Storehouse Capacity 10,800 G. 27
Total cost, \$ 2371. Date completed Sept. 25, 1941
Material: Walls Wood Foundation Concrete
Roof Wood & Prepared Roofing on Wood Floors Concrete
Total floor area above basement, square feet 1350 sq. ft.
Size: Main building 54'-2" x 25' x 4' Wings None Basement None
a None Height of first floor above ground 1'
(How heated)
b None How lighted Electric
(Type of heat)
c None Water connections None
(Type of domestic hot water heater)
Sewer connections None
Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas None
Electric None
Ice None

METERS INSTALLED
(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.



Post Plan No. None

O.O.M.G.: Plan No. 800-661 Building No. T-8

Place Fort Revere, Hull, Mass.
Designation of building Single storehouse & Co. Adm. (2 adjoining) Capacity 15,784 Cu. Ft.
Total cost, \$5,854.00 Date completed August 25, 1941
Material: Walls Wood Foundation Concrete
Roof Wood and prepared roofing on Wood Floors Concrete
Total floor area above basement, square feet 1975 sq. ft.
Size: Main building 78'4" x 25'4" Wings None Basement None
a Common Stoves Height of first floor above ground 12"
(How heated)
b Forced warm air How lighted Electric
(Type of heat)
c None Water connections 1"
(Type of domestic hot water heater) Sewer connections 4"
Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

(Give quantity and size)	
Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED

(Give quantity and size)

Gas _____ None _____

Electric _____ None _____

Ice _____ None _____

METERS INSTALLED

(Give quantity and capacity)	
Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.

"b" State whether steam, vapor, hot water, or hot air.

"c" State whether gas, coal, oil, or central heating plant.

See reverse side of form.

O.Q.M.G.: Plan No. 700-1165 Building No. T 9

COOKING RANGES INSTALLED
(Give quantity and size)

REFRIGERATORS INSTALLED
(Give quantity and size)


METERS INSTALLED

(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

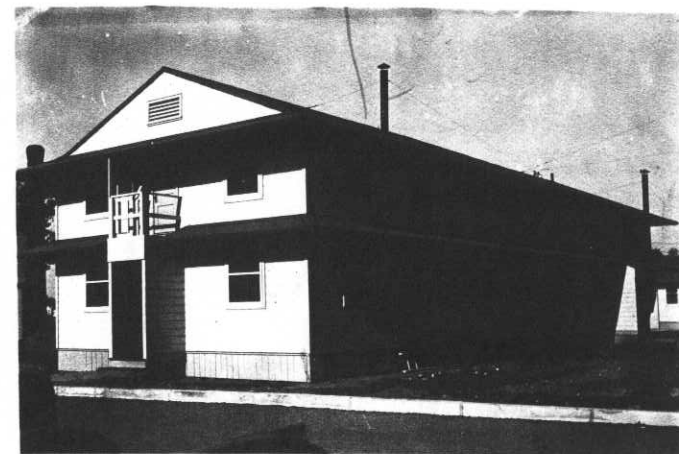[illegible]

"b" State whether steam, vapor, hot water, or hot air.

"c" State whether gas, coal, oil, or central heating plant.

O.Q.M.G.: Plan No. 700-1165 Building No. T 10

A black and white photograph of a two-story building, likely a schoolhouse, with a prominent chimney and a small American flag on the roof. The building has a dark, steeply pitched roof and light-colored siding. A small American flag is mounted on the front-facing gable. A large, dark chimney is visible on the right side of the roof. The building has several windows, some of which are dark, suggesting they are closed or the interior is dark. A small porch or entrance is visible on the left side. The overall image has a high-contrast, grainy quality, typical of older black and white photography.

METERS INSTALLED

(Give quantity and capacity)

Gas None

Electric	None
----------	------

Electric
Oil	None

Oil ----- None
 Grease ----- None

Steam -----None

Water -----None

(Below enter chronologically all modifications, additions, introductions of w

[illegible]

"b" State whether steam, vapor, hot water, or hot air.

"c" State whether gas, coal, oil, or central heating plant.

Post Plan No. None

O.Q.M.G.: Plan No. 700-439 Building No. T-11

Place Fort Revere, Hull, Massachusetts
Designation of building Fire House Capacity 2 Trucks
Total cost, \$ 1411.00 Date completed Sept. 25, 1941
Material: Walls Wood Foundation Concrete Piers
Roof Prepared roofing on wood Floors Concrete
Total floor area above basement, square feet 600 sq. ft.
Size: Main building 25'-6" x 24'-6" Wings None Basement None
a None Height of first floor above ground 4"
(How heated)
b None How lighted Electric
(Type of heat)
Water connections None
c None Sewer connections None
(Type of domestic hot water heater)
Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas None

Electric None

Ice None


METERS INSTALLED
(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

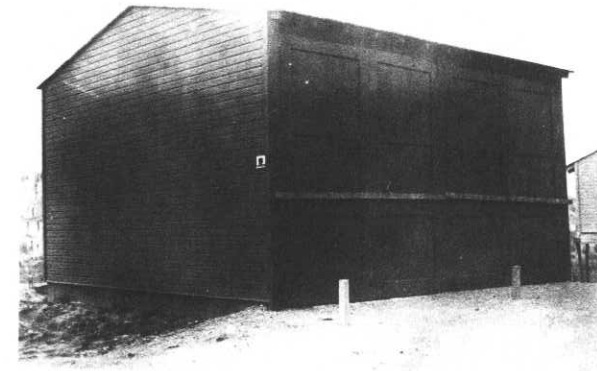[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 800-561 Building No. T-12

Place Fort Revere, Hull, Mass.

Designation of building Post Exchange E-2 Capacity 18,240 G.W.

Total cost, \$ 9,470.00 Date completed August 25, 1941

Material: Walls Wood Foundation ** Wood and Concrete

Roof ~~Wood~~ and prepared roofing on Wood Floors *Wood and Concrete

Total floor area above basement, square feet 2280 sq. ft.

Size: Main building 63' x 37' Wings None Basement None

a Individual heating system Height of first floor above ground 1 ft.
(How heated)

b Steam How lighted Electric
(Type of heat)

c Coal Water connections 1 1/2"
(Type of domestic hot water heater) Sewer connections 6"

Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

(Give quantity and size)	
Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED

(Give quantity and size)

Gas _____ None _____

Electric _____ None _____

Ice _____ None _____

METERS INSTALLED

(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)


ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

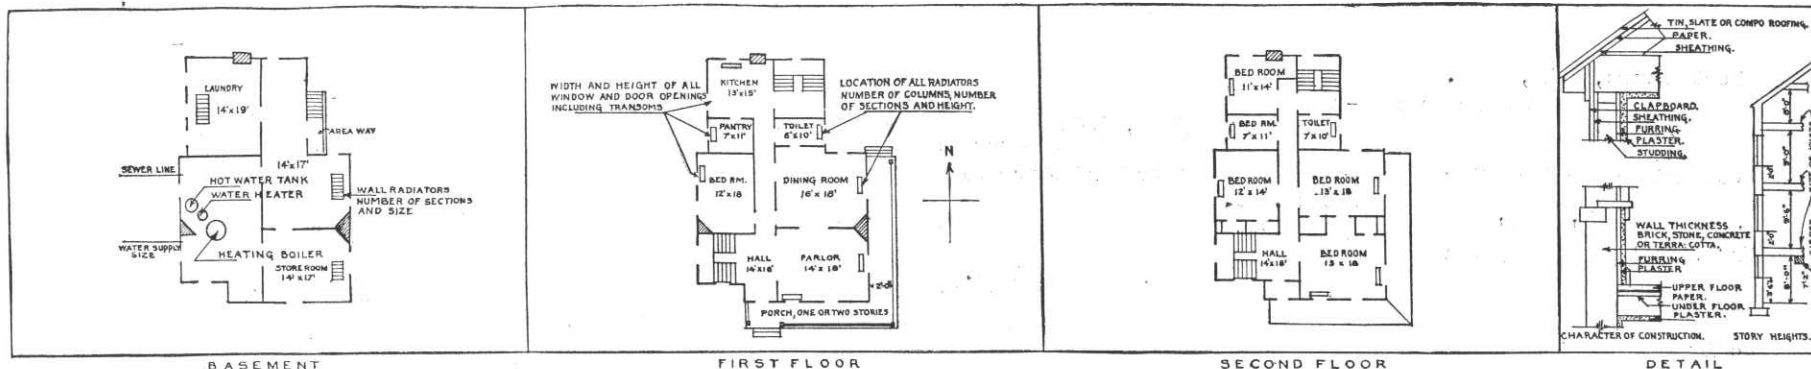

IN SPACE BELOW SKETCH BASEMENT AND FLOOR PLANS OF BUILDINGS, GIVING DATA AS PER PLANS ABOVE

REMARKS

*Floors in heater room, toilet and shower rooms are concrete - other floors 2 1/2" matched flooring.

**Concrete piers with the exception of the heater, toilet and shower rooms which have concrete foundation walls.

Note: For building plan see OCMG Drawing #899-561

INSTRUCTIONS

If plans of building are available, forward copy of same showing information called for above. These plans should be checked against the building and any variations from same in the building as constructed should be noted.

If plans are not available make sketch plans and elevation in spaces above. The plans shown are typical of "quarters." Similar plans may be made for all types of buildings. There are 10 squares to the inch. Each square will represent 1', 2', 4', or 8', etc., as may be necessary to show entire building in the space allowed. Show inside dimensions and designation of each room. Indicate location of water and sewer connections. In space under heading "Details" show character of construction, story heights, etc.

Post Plan No. None

O.Q.M.G.: Plan No. 700-1133 Building No. T-13

Place Fort Revere, Massachusetts
Designation of building Mass Hall Capacity 170
Total cost, \$ 6189.00 Date completed August 25, 1941
Material: Walls Wood Foundation Concrete piers
Roof Wood and prepared roofing on Wood Floors Wood
Total floor area above basement, square feet 2231
Size: Main building 37'-4" x 25'-4" Wings None Basement None
a Stoves (How heated) Height of first floor above ground 12"
b Cannon (Type of heat) How lighted Electric
Water connections 2"
c Booster Boiler (Type of domestic hot water heater) Sewer connections 6"
Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

(Give quantity and size)

Coal	3-75 Army Ranges
Gas	None
Electric	Deep fat fryer
Oil	None
Steam	None

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas None
Electric None
Ice 1-#6 1-#7

METERS INSTALLED
(Give quantity and capacity)

(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 700-1165 Building No. T 14

Place Fort Revere, Hull, Mass.
Designation of building Barracks Capacity 63 Men
Total cost, \$ 9,117.00 Date completed August 25, 1941
Material: Walls Wood Foundation ** Concrete
Roof Wood and Prepared Roofing on Wood Floors * Wood
Total floor area above basement, square feet 4,720 Sq. Ft.
Size: Main building 80'x29'-6" Approx. Wings None Basement None
a Individual Heating Plants 23 Height of first floor above ground 12"
(How heated)
b Forced Warm Air How lighted Electric
(Type of heat)
Coal Water connections 2"
c Sewer connections 6"
(Type of domestic hot water heater) Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas.....None
Electric.....None
Ice.....None

METERS INSTALLED
(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water)


[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.

"b" State whether steam, vapor, hot water, or hot air.

"c" State whether gas, coal, oil, or central heating plant.

See reverse side of form.

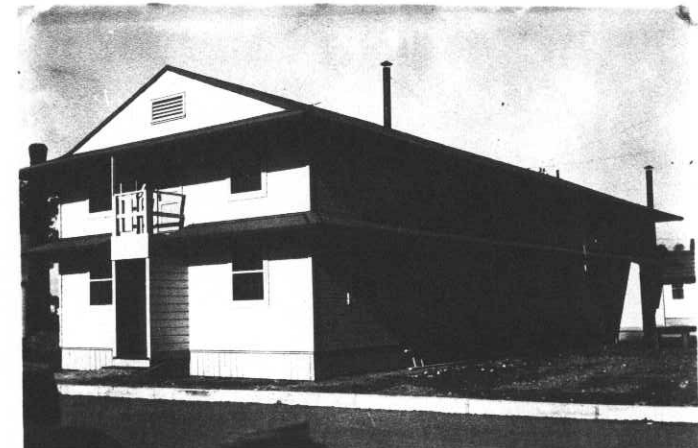

Post Plan No. None

O.Q.M.G.: Plan No. 700-1165 Building No. T 15

Place Fort Revere, Hull, Mass.
 Designation of building Barracks Capacity 63 Men
 Total cost, \$ 9,117.00 Date completed August 25, 1941
 Material: Walls Wood Foundation ** Concrete
Roof ~~Wood and~~ Prepared Roofing on ~~Wood~~ Floors * Wood
 Total floor area above basement, square feet 4,720 Sq. Ft.
 Size: Main building 80'x29'-6" Approx. Wings None Basement None
 a Individual Heating Plants 23 Height of first floor above
 (How heated) ground 12"
 b Forced Warm Air How lighted Electric
 (Type of heat) Coal Water connections 2"
 c Coal Sewer connections 6"
 (Type of domestic hot water heater) Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED

(Give quantity and size)


Gas None

Electric None

Ice None

METERS INSTALLED

Gas _____ None _____
Electric _____ None _____
Oil _____ None _____
Steam _____ None _____
Water _____ None _____

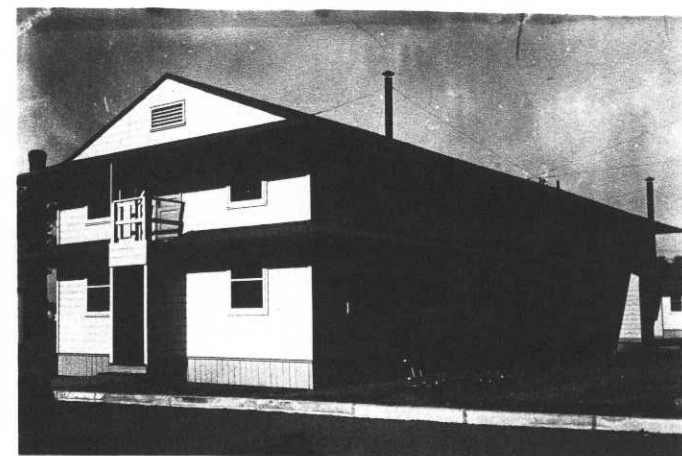

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 800-661 Building No. T-16

Place Fort Revere, Hull, Mass.

Designation of building Single Storehouse & Co. Adm. (2 adjoining) Capacity 15,784 Cu. Ft

Total cost, \$ 5,854.00 Date completed August 25, 1941

Total cost, \$ 3,100.00 Date completed 3-1-58
Material: Walls Wood Foundation Concrete

Material: Walls _____ Foundation _____
Roof: Wood and prepared roofing on Wood Floors _____ Concrete _____

Total floor area above basement, square feet 1973 sq. ft.

Size: Main building 73'4" x 25'4" Wings None Basement None

Size: Main building _____ Wings _____ Basement _____
 a Common stoves _____ Height of first floor above _____

a. Common Stoves (How heated) _____ Height of first floor above ground 12"

b Forced warm air _____ ground _____
How lighted _____ Electric _____

(Type of heat)

Water connections	2 1/2"
Sewer connections	4"

c. _____
(Type of domestic hot water heater)

COOKING RANGES INSTALLED **REFRIGERATORS INSTALLED** **METERS INSTALLED**

COOKING RANGES INSTALLED (Give quantity and size) **REFRIGERATORS INSTALLED** (Give quantity and size) **METERS INSTALLED** (Give quantity and capacity)

Coal _____ None _____ Gas _____ None _____

Gas	None	Electric	None	Electric	None
-----	------	----------	------	----------	------

Electric None Ice None Oil None

Oil	None	Steam	None
-----	------	-------	------

Steam	None	Water	None
-------	------	-------	------

[illegible]

Approval of Secretary of War
Recommended by A. B. 20, 1425

as required by A. R. 30-1435
(Give date and File Number)

(Give date and File Number) _____ (Below enter chronologically all modifications, additions, deletions, and other changes to the original plan, including introductions of water, sewer, lights, heating, etc.)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—"a" State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.

"b" State whether steam, vapor, hot water, or hot air.

"c" State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 700-1165 Building No. F 17

Place Fort Revere, Hull, Mass.
Designation of building Barracks Capacity 63 Men
Total cost, \$ 9,117.00 Date completed August 25, 1941
Material: Walls Wood Foundation ** Concrete
Roof Wood and Prepared Roofing on Wood Floors * Wood
Total floor area above basement, square feet 4,720 Sq. Ft.
Size: Main building 80'x29'-6" Approx Wings None Basement None
a Individual Heating Plants 23' Height of first floor above ground 12"
(How heated)
b Forced Warm Air How lighted Electric
(Type of heat)
Water connections 2"
c Coal Sewer connections 6"
(Type of domestic hot water heater) Gas connections None

COOKING RANGES INSTALLED

(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED

(Give quantity and size)

Gas None

Electric None

Ice None

METERS INSTALLED

(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

ADDITIONS AND INSTALLATION

(Below enter chronologically all modifications, additions, introductions of w


[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.

"b" State whether steam, vapor, hot water, or hot air.

"c" State whether gas, coal, oil, or central heating plant.


See reverse side of form.

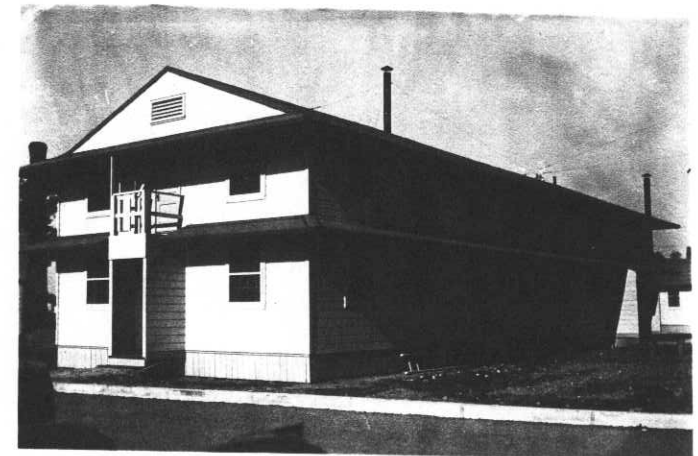

O.Q.M.G.: Plan No. 700-1165 Building No. T 18

[illegible]

See reverse side of form.

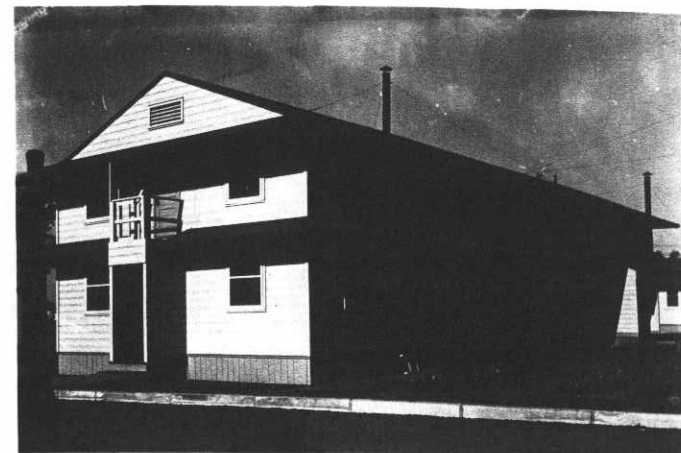

Post Plan No. None

O.Q.M.G.: Plan No. 700-1165 Building No. T 19

Place Fort Revere, Hull, Mass. Capacity 63 Men
 Designation of building Barracks
 Total cost, \$ 9,117.00 Date completed August 25, 1941
 Material: Walls Wood Foundation ** Concrete
 Roof Wood and Prepared Roofing on Wood Floors * Wood
 Total floor area above basement, square feet 4,720 Sq. Ft.
 Size: Main building 80'x29'-6" Approx. Wings None Basement None
 a Individual Heating Plants Height of first floor above ground 12"
 (How heated)
 b Forced Warm Air How lighted Electric
 (Type of heat)
 c Coal Water connections 2"
 (Type of domestic hot water heater) Sewer connections 6"
 Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

(Give quantity and size)

Coal.....None.....
Gas.....None.....
Electric.....None.....
Oil.....None.....
Steam.....None.....

REFRIGERATORS INSTALLED

(Give quantity and size)

Gas _____ None _____

Electric _____ None _____

Ice _____ None _____

METERS INSTALLED


(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

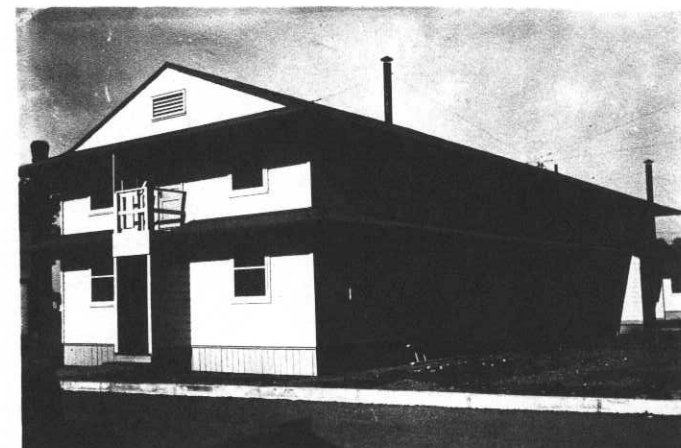[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 700-1165 Building No. T-20

Place Fort Revere, Hull, Mass.
Designation of building Barracks Capacity 63 men
Total cost, \$ 9,117.00 Date completed August 25, 1941
Material: Walls Wood Foundation **Concrete
Roof Wood and prepared roofing on Wood Floors *Wood
Total floor area above basement, square feet 4720 sq. ft.
Size: Main building 80'x29'-6"approx. Wings None Basement None
a Individual Heating Plants 23'High Height of first floor above
(How heated) ground 12"
b Forced Warm Air How lighted Electric
(Type of heat) Water connections 2"
c Coal Sewer connections 6"
(Type of domestic hot water heater) Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal None
Gas None
Electric None
Oil None
Steam None

REFRIGERATORS INSTALLED

(Give quantity and size)

Gas None

Electric None

Ice None

METERS INSTALLED


(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

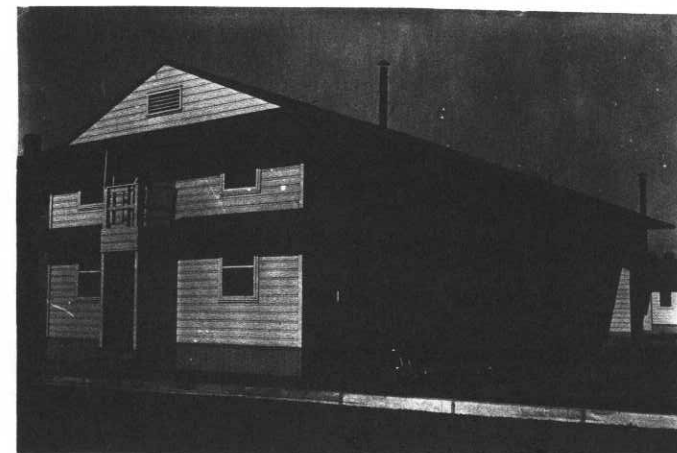[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 700-1133 Building No. T-21

Place Fort Revere, Massachusetts
Designation of building Mess Hall Capacity 170
Total cost, \$ 6182.00 Date completed August 25, 1941
Material: Walls Wood Foundation Concrete piers
Roof Wood and prepared roofing on Wood Floors Wood
Total floor area above basement, square feet 2231
Size: Main building 37'-4" x 25'-4" Wings None Basement None
a Stoves (How heated) Height of first floor above ground 12"
b Cannon (Type of heat) How lighted Electric
c Booster Boiler (Type of domestic hot water heater) Water connections 2"
Sewer connections 6"
Gas connections None

COOKING RANGES INSTALLED

REFRIGERATORS INSTALLED

METERS INSTALLED

(Give quantity and size)

Coal 3-#5 Army Ranges

Gas None

Electric Deep fat fryer

Oil None

Steam None

(Give quantity and size)

Gas None

Electric None

Ice 1-16 1-17

(Give quantity and capacity)
 Gas _____ None _____
 Electric _____ None _____
 Oil _____ None _____
 Steam _____ None _____
 Water _____ None _____

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)


ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

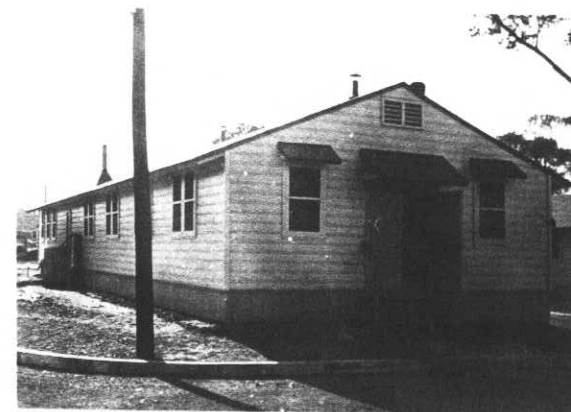

O.Q.M.G.: Plan No. 700-1133 Building No. T-22

A black and white photograph of a long, single-story wooden building, likely a schoolhouse, with a gabled roof and multiple windows. A tall wooden pole stands in the foreground on the left. The building has a weathered appearance with horizontal siding. There are several windows visible along the side, and a small vent or chimney is on the roof. The foreground shows a dirt or gravel area with a low curb.

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 700-1133 Building No. T-23

Place Fort Revere, Massachusetts
Designation of building Mess Hall Capacity 170
Total cost, \$ 6189.00 Date completed August 25, 1941
Material: Walls Wood Foundation Concrete piers
Roof Wood and prepared roofing on Wood Floors Wood
Total floor area above basement, square feet 2231
Size: Main building 37'-4"x25'-4" Wings None Basement None
a Stoves (How heated) _____ Height of first floor above ground 12"
b Cannon (Type of heat) _____ How lighted Electric
Water connections 2"
c Booster Boiler (Type of domestic hot water heater) _____ Sewer connections 6"
Gas connections None

COOKING RANGES INSTALLED
(Give quantity and size)

Coal 3-75 Army Ranges
Gas None
Electric Deep fat fryer
Oil None
Steam None

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas None
Electric None
Ice 1-16 1-17

METERS INSTALLED
(Give quantity and capacity)

Gas	None
Electric	None
Oil	None
Steam	None
Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.


O.Q.M.G.: Plan No. 700-1165 Building No. T-24

COOKING RANGES INSTALLED (Give quantity and size)		REFRIGERATORS INSTALLED (Give quantity and size)		METERS INSTALLED (Give quantity and capacity)	
Coal	None	Gas	None	Gas	None
Gas	None	Electric	None	Electric	None
Electric	None	Ice	None	Oil	None
Oil	None			Steam	None
Steam	None			Water	None

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

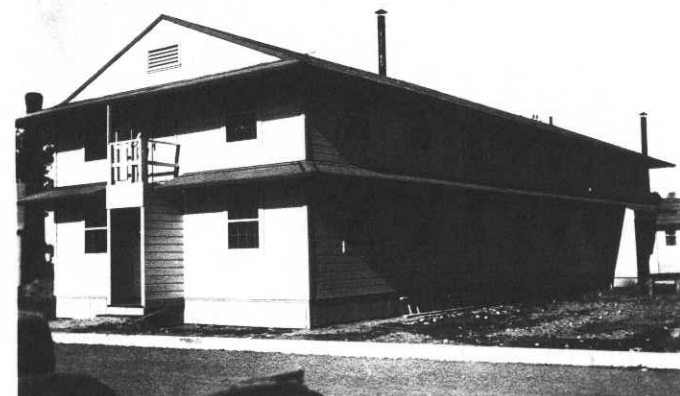[illegible]


INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

O.Q.M.G.: Plan No. 700-1165 Building No. T-25

[illegible]

See reverse side of form.

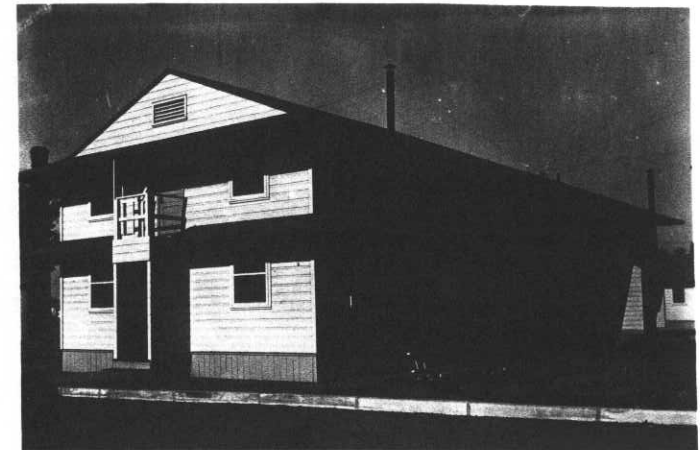

Post Plan No. None

O.Q.M.G.: Plan No. Y00-459 Building No. T-26

Place Fort Revere, Massachusetts
Designation of building Recreation Building A-5 Capacity 100-Men
Total cost, \$ 3795.00 Date completed August 25, 1941
Material: Walls Wood Foundation **Concrete
Roof Wood & prepared roofing on 1/2 Floors *Concrete and wood
Total floor area above basement, square feet 1120
Size: Main building 45'-2"x25'-4" Wings None Basement None
a Indiv. Htg. System Height of first floor above ground 12"
(How heated)
b Forced Warm Air How lighted Electric
(Type of heat)
Water connections None
c None Sewer connections "
(Type of domestic hot water heater) Gas connections "

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	None
Electric	None
Oil	None
Steam	None

REFRIGERATORS INSTALLED
(Give quantity and size)

Gas None
Electric "
Ice "

METERS INSTALLED
(Give quantity and capacity)

Gas	None
Electric	"
Oil	"
Steam	"
Water	"

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)


[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.

O.Q.M.G.: Plan No. 800-459 Building No. T-27

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

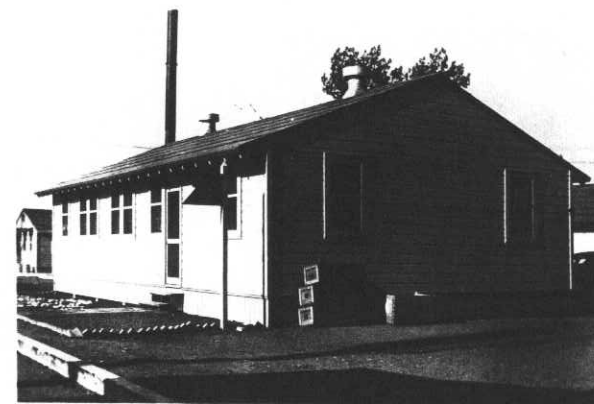[illegible]

See reverse side of form.

Post Plan No. None

O.Q.M.G.: Plan No. 800-459 Building No. T-28

Place Port Revere, Massachusetts
Designation of building Recreation Building A-5 Capacity 100-Men
Total cost, \$ 3795.00 Date completed August 25, 1941
Material: Walls Wood Foundation ** Concrete
Roof Wood and prepared roofing on Wood Floors * Concrete and wood
Total floor area above basement, square feet 1120
Size: Main building 45'-2"x25'-4" Wings None Basement None
a Indiv. Htg. System (approx. 14') Height of first floor above ground 12"
b Forced warm air (Type of heat) How lighted Electric
c None (Type of domestic hot water heater) Water connections None
Sewer connections "
Gas connections "

COOKING RANGES INSTALLED
(Give quantity and size)

Coal	None
Gas	"
Electric	"
Oil	"
Steam	"

REFRIGERATORS INSTALLED

(Give quantity and size)

Gas _____ None _____

Electric _____ " _____

Ice _____ " _____

METERS INSTALLED


(Give quantity and capacity)

Gas	None
Electric	"
Oil	"
Steam	"
Water	"

Approval of Secretary of War
as required by A. R. 30-1435
(Give date and File Number)

ADDITIONS AND INSTALLATIONS

(Below enter chronologically all modifications, additions, introductions of water, sewer, lights, heating, etc.)

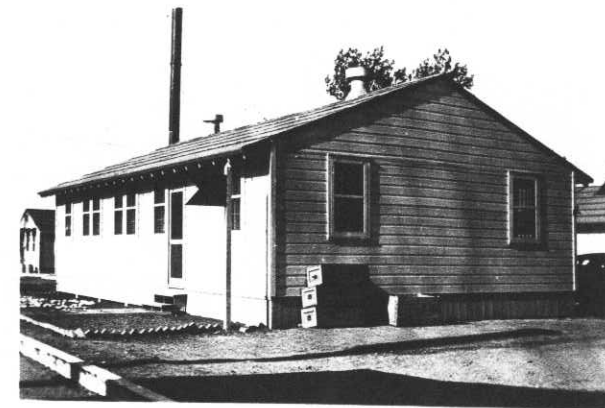[illegible]

INSTRUCTIONS.—“a” State whether heated from central heating or by individual heating plants, stoves, furnaces, or fireplaces.
 “b” State whether steam, vapor, hot water, or hot air.
 “c” State whether gas, coal, oil, or central heating plant.

See reverse side of form.
